



WEEKLY SUMMARY REPORT – CONTRACT WEEK 04

21-036 EAST NAPLES BAY

DREDGING AND ROCK REMOVAL PROJECT



Date: 11/8/2021 to 11/12/2021			
Inspectors: Sam Boyd	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Days of Week: Monday to Friday	Contract Days: 22 to 26	Total Days: 365	Accident Report #: N/A
Canal(s) Worked In: CC-CC	Stations Worked Between: 1+00 to 3+00		

General

Remarks

#1 – Prime Contractor – Quality Enterprises:

Monday 11-8-2021:

- Contractor’s equipment is staged in canal CC-CC towards the west end of the canal (between stations 1+00 and 2+00). This equipment includes an excavator mounted on the barge, a hopper, a push boat, and a support boat. Contractor also has another excavator staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor installed turbidity curtain.
- Contractor grinded rock in Canal CC-CC from stations 1+00 to 2+00 with the 323 excavator.
- Push boat was used to position the 323 excavator for grinding rock.
- 326 excavator removed material from station 1+50 and placed material in hopper.
- Contractor had another excavator delivered at the empty lot on 1300 Curlew Avenue and then picked the excavator back up by another truck.
- Contractor continued to grind rock with the 323 excavator with push boat helping with positioning.
- The 326 excavator was used to remove material from station 1+50 and transfer it to the dewatering site on the empty lot at 1300 Curlew Avenue.
- Contractor finished work for the day and left the barge, excavator, support boat, push boat, and hopper in canal CC-CC near station 1+50. The contractor left the 326 excavator on the empty lot.

Tuesday 11-9-2021:

- Contractor’s equipment is staged in canal CC-CC towards the west end of the canal (between stations 1+50 and 2+00). This equipment includes an excavator mounted on the barge, a hopper, a push boat, and a support boat. Contractor also has two other excavators, and a water truck staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Water truck came to the empty lot at 1300 Curlew Avenue.
- Contractor installed turbidity curtain.
- Contractor grinded rock with the 323 excavator at station 2+50 from 8:00 am to 8:45 am.
- Transport truck came to the empty lot at 1300 Curlew Avenue with two fuel cubes.
- Contractor moved fuel cubes to the southwest corner of the empty lot at 1300 Curlew Avenue.
- Dump truck came to the empty lot and got stuck. Contractor used 326 excavator to tow the truck out. The truck



WEEKLY SUMMARY REPORT – CONTRACT WEEK 04

21-036 EAST NAPLES BAY

DREDGING AND ROCK REMOVAL PROJECT



left after it was released.

- Contractor grinded rock with the 323 excavator at station 1+50 from 10:00 am to 11:45 am.
- A fuel truck came to the empty lot at 1300 Curlew Avenue to fill up the two fuel cubes.
- A utility truck came to the empty lot at 1300 Curlew Avenue to continue setting up the fuel cubes and to install solar panels on the large fuel cube to charge its battery.
- Contractor grinded rock with the 323 excavator between stations 1+50 to 3+00 from 1:00 pm to 4:30 pm.
- Contractor finished work for the day and left the barge, excavator, support boat, push boat, and hopper in canal CC-CC near station 2+00. The contractor left the 326 excavator, the front end loader, the water truck, and the two fuel cubes on the empty lot.

Wednesday 11-10-2021:

- Contractor's equipment is staged in canal CC-CC towards the west end of the canal (between stations 2+00 and 2+50). This equipment includes an excavator mounted on the barge, a hopper, a push boat, and a support boat. Contractor also has two other excavators, two fuel cubes, and a water truck staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor grinded rock with the 323 excavator at station 3+00 from 8:00 am to 8:45 am.
- Utility truck and technician came at 9:00 am.
- Contractor used the small fuel cube to fill the 326 excavator and the front end loader with fuel.
- Contractor used 326 excavator to transport small fuel cube from the south side of the empty lot at 1300 Curlew Avenue to the push boat.
- Contractor used push boat to transport small fuel cube to the barge so that 323 excavator could fill its tank.
- Push boat was used to transport small fuel cube within reach of the 326 excavator which then moved it back to its location at the south side of the empty lot at 1300 Curlew Avenue.
- Contractor used the 323 excavator to grind rock at station 2+50 from 10:00 am to 12:00 pm.
- Contractor resumed grinding rock between stations 2+50 and 3+00 from 1:15 pm to 5:00 pm.
- Contractor finished work for the day and left the barge, excavator, support boat, push boat, and hopper in canal CC-CC near station 3+00. The contractor left the 326 excavator, the front end loader, the water truck, and the two fuel cubes on the empty lot.

Thursday 11-11-2021:

- Contractor's equipment is staged in canal CC-CC towards the west end of the canal (between stations 2+00 and 2+50). This equipment includes an excavator mounted on the barge, a hopper, and a push boat. Contractor also has two other excavators, two fuel cubes, and a water truck staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor installed turbidity curtain across the mouth of Canal CC-CC.
- Contractor grinded rock with the 323 excavator at station 3+00 from 8:30 am to 12:00 pm.
- Contractor brought the support boat to the empty lot at 1300 Curlew Avenue by truck and left it staged on



WEEKLY SUMMARY REPORT – CONTRACT WEEK 04

21-036 EAST NAPLES BAY

DREDGING AND ROCK REMOVAL PROJECT



land.

- Contractor removed turbidity curtain from mouth of Canal CC-CC to let another contractor with a barge, crane, and excavator enter the canal. Contractor re-installed turbidity curtain after other contractor had entered Canal CC-CC.
- Contractor inspected the Epiroc grinder for signs of damage and removed the grinder from the 323 excavator and used the front end loader to place it on the southwest corner of the empty lot at 1300 Curlew Avenue.
- Contractor put the bucket on the 323 excavator and removed rock and sediment from station 3+00 and placed the sediment into the hopper.
- Push boat moved the hopper to the edge of the empty lot at 1300 Curlew Avenue.
- Contractor transferred dredged material from the hopper to the dewatering site on the empty lot at 1300 Curlew Avenue.
- Utility truck came to the empty lot at 1300 Curlew Avenue at 3:30 pm.
- Contractor finished work for the day and left the barge, 323 excavator, support boat, and hopper in canal CC-CC near station 2+00. The contractor left the 326 excavator, the front end loader, the water truck, the support boat, and the two fuel cubes on the empty lot.

Friday 11-12-2021:

- Contractor's equipment is staged in canal CC-CC towards the west end of the canal (between stations 1+50 and 2+00). This equipment includes an excavator mounted on the barge, a hopper, and a push boat. Contractor also has two other excavators, two fuel cubes, a support boat, and a water truck staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Collier Seawall and Dock's barge and push boat passed contractor's equipment staged between stations 1+50 and 2+00 as it exited Canal CC-CC at 8:00 am
- Contractor inspected and greased the 323 excavator and the 326 excavator.
- Contractor cleaned the 323 excavator, 326 excavator, hopper, and push boat with water from the water truck.
- Contractor finished work for the day at 9:30 am and left the barge, 323 excavator, push boat, and hopper in canal CC-CC between stations 1+50 and 2+00. The contractor left the 326 excavator, the front end loader, the water truck, the support boat, and the two fuel cubes on the empty lot.

Note: Daily reports with pictures attached for the week.



DAILY REPORT OF CONSTRUCTION
21-036 EAST NAPLES BAY
DREDGING AND ROCK REMOVAL PROJECT



Date: 11/8/2021			
Inspectors: SB	Stantec PIN: 2028113191	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: Monday	Contract Day: 22/365	Week: 4	Accident Report #: N/A
High Temp (°F): 73°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 4:42 PM – +2.4'
Low Temp (°F): 59°F	Wind: 11mph	Wind: 12mph	Low Tide: 9:44 AM – -0.4'
Canal Worked In: CC-CC	Stations Worked Between:	1+00 to 2+00	

General

#1 – Prime Contractor – Quality Enterprises:

- Contractor's equipment is staged in canal CC-CC towards the west end of the canal (between stations 1+00 and 2+00). This equipment includes an excavator mounted on the barge, a hopper, a push boat, and a support boat. Contractor also has another excavator staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor installed turbidity curtain across the mouth of canal CC-CC.
- Contractor grinded rock in Canal CC-CC from stations 1+00 to 2+00 with the 323 excavator.
- Push boat was used to position the 323 excavator for grinding rock.
- 326 excavator removed material from station 1+50 and placed material in hopper.
- Contractor had another excavator delivered at the empty lot on 1300 Curlew Avenue and then picked the excavator back up by another truck.
- Contractor continued to grind rock with the 323 excavator with push boat helping with positioning.
- The 326 excavator was used to remove material from station 1+50 and transfer it to the dewatering site on the empty lot at 1300 Curlew Avenue.
- Contractor finished work for the day and left the barge, excavator, support boat, push boat, and hopper in canal CC-CC near station 1+50. The contractor left the 326 excavator on the empty lot.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	1	2.5	Boat Captain	1	9	Foreman	0	0
		Excavator Operator	1	9	Truck Driver	1	1	Assistant	1	9
		Technician	0	0	Superintendent	1	9	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	9
1	CAT 326	Excavator	1	1	3
1	02016	Front End Loader	1	1	0.25
1	FL6223TB	Push Boat	1	1	5
1	FL2474PP	Support Boat	1	1	2
1	N6143X	Fuel Truck	1	0	0
1	P9457E	Water Truck	1	1	0
1	Z67EAZ	Dump truck	1	1	0
1	MB38DQ	Utility Truck	1	1	0
1	5178CR	Transport Truck	1	1	1

Visitors			
Name	Company	Hours at Job Site	
		From:	To:
Jack Hooper	Quality Enterprises	8:00 AM	9:30 AM
Jack Hooper	Quality Enterprises	2:30 PM	3:30 PM

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT – Inspector	From: 8:00 AM	To: 4:30 PM	8.5 hours

E 90 SE 120 150 S 180 S 210

☀ 153°SE (T) ● 26°8'13"N, 81°47'16"W ±52ft ▲ 7ft



323 excavator on barge attached to push boat

SE S SW
120 150 180 210 240

☀ 176°S (T) ● 26°8'13"N, 81°47'16"W ±39ft ▲ 8ft



08 Nov 2021, 08:27:08


Checking hoses on 323 excavator



☀ 182°S (T) ☉ 26°8'13"N, 81°47'15"W ±19ft ▲ 8ft




323 excavator grinding rock near station 1+50



☉ 235°SW (T) ☉ 26°8'13"N, 81°47'15"W ±13ft ▲ 8ft



323 excavator on barge grinding rock at station 1+50



☉ 137°SE (T) ● 26°8'13"N, 81°47'16"W ±13ft ▲ 7ft



08 Nov 2021, 14:56:12

323 excavator lifting spud to allow push boat to move the barge



☉ 127°SE (T) ● 26°8'13"N, 81°47'16"W ±19ft ▲ 7ft



Turbidity curtain across the mouth of Canal CC-CC. 323 excavator grinding rock at station 2+00



Hopper tied up to barrier walls at the south side of the empty lot at 1300 Curlew Avenue




NW N NE
00 330 0 30 60

☀ 11°N (T) ☉ 26°8'14"N, 81°47'16"W ±62ft ▲ 9ft

08 Nov 2021, 15:19:15

Transport truck bringing front end loader to empty lot at 1300 Curlew Avenue




☉ 213°SW (T) ● 26°8'14"N, 81°47'15"W ±19ft ▲ 8ft



08 Nov 2021, 16:24:41

Dewatering site at the south side of the empty lot at 1300 Curlew Avenue



☀ 124°SE (T) ● 26°8'13"N, 81°47'15"W ±26ft ▲ 8ft



08 Nov 2021, 16:25:40

323 excavator grinding rock at station 2+50



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 11/9/2021			
Inspectors: SB	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Tuesday	Contract Day: 23/365	Week: 4	Accident Report #: N/A
High Temp (°F): 76°F	AM Conditions: Sunny	PM Conditions: Partly-Cloudy	High Tide: 5:56 PM – +2.3'
Low Temp (°F): 59°F	Wind: 7mph	Wind: 14mph	Low Tide: 10:42 AM – -0.2'
Canal Worked In: CC-CC	Stations Worked Between:	1+00 to 3+00	

General
<p>#1 – Prime Contractor – Quality Enterprises:</p> <ul style="list-style-type: none"> Contractor’s equipment is staged in canal CC-CC towards the west end of the canal (between stations 1+50 and 2+00). This equipment includes an excavator mounted on the barge, a hopper, a push boat, and a support boat. Contractor also has two other excavators, and a water truck staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102. Water truck came to the empty lot at 1300 Curlew Avenue. Contractor installed turbidity curtain across the mouth of Canal CC-CC. Contractor grinded rock with the 323 excavator at station 2+50 from 8:00 am to 8:45 am. Transport truck came to the empty lot at 1300 Curlew Avenue with two fuel cubes. Contractor moved fuel cubes to the southwest corner of the empty lot at 1300 Curlew Avenue. Dump truck came to the empty lot and got stuck. Contractor used 326 excavator to tow the truck out. The truck left after it was released. Contractor grinded rock with the 323 excavator at station 1+50 from 10:00 am to 11:45 am. A fuel truck came to the empty lot at 1300 Curlew Avenue to fill up the two fuel cubes. A utility truck came to the empty lot at 1300 Curlew Avenue to continue setting up the fuel cubes and to install solar panels on the large fuel cube to charge its battery. Contractor grinded rock with the 323 excavator between stations 1+50 to 3+00 from 1:00 pm to 4:30 pm. Contractor finished work for the day and left the barge, excavator, support boat, push boat, and hopper in canal CC-CC near station 2+00. The contractor left the 326 excavator, the Front end loader, the water truck, and the two fuel cubes on the empty lot.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	1	1	Boat Captain	1	9	Foreman	0	0
		Excavator Operator	1	9	Truck Driver	3	4	Assistant	1	9
		Technician	1	3	Superintendent	1	9	VP	1	0.25

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	9
1	CAT 326	Excavator	1	1	1
1	02016	Front End Loader	1	1	2
1	FL6223TB	Push Boat	1	1	5
1	FL2474PP	Support Boat	1	1	2
1	N6143X	Fuel Truck	1	1	1
1	P9457E	Water Truck	1	1	1
1	Z67EAZ	Dump truck	1	1	0.25
1	MB38DQ	Utility Truck	1	1	3
1	5178CR	Transport Truck	1	1	1

Visitors			
Name	Company	Hours at Job Site	
		From:	To:
Jack Hooper	Quality Enterprises	8:00 AM	9:00 AM
Lou Gaudio	Quality Enterprises	11:00 AM	11:15 AM

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT – Inspector	From: 8:00 AM	To: 4:30 PM	8.5 hours

S SW W
150 180 210 240 270
☀ 215°SW (T) ● 26°8'14"N, 81°47'15"W ±29ft ▲ 9ft



Water truck parked on the empty lot at 1300 Curlew Avenue



☀ 184°S (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 9ft




09 Nov 2021, 08:01:38

Turbidity curtain across the mouth of Canal CC-CC

N 0 30 60 90 120
NE E
☀ 55°NE (T) ● 26°8'14"N, 81°47'16"W ±36ft ▲ 8ft




Front end loader moving large fuel cube from transport truck to empty lot at 1300 Curlew Avenue




☀ 110°E (T) ● 26°8'14"N, 81°47'16"W ±26ft ▲ 8ft



Front end loader moving large fuel cube from transport truck to empty lot at 1300 Curlew Avenue

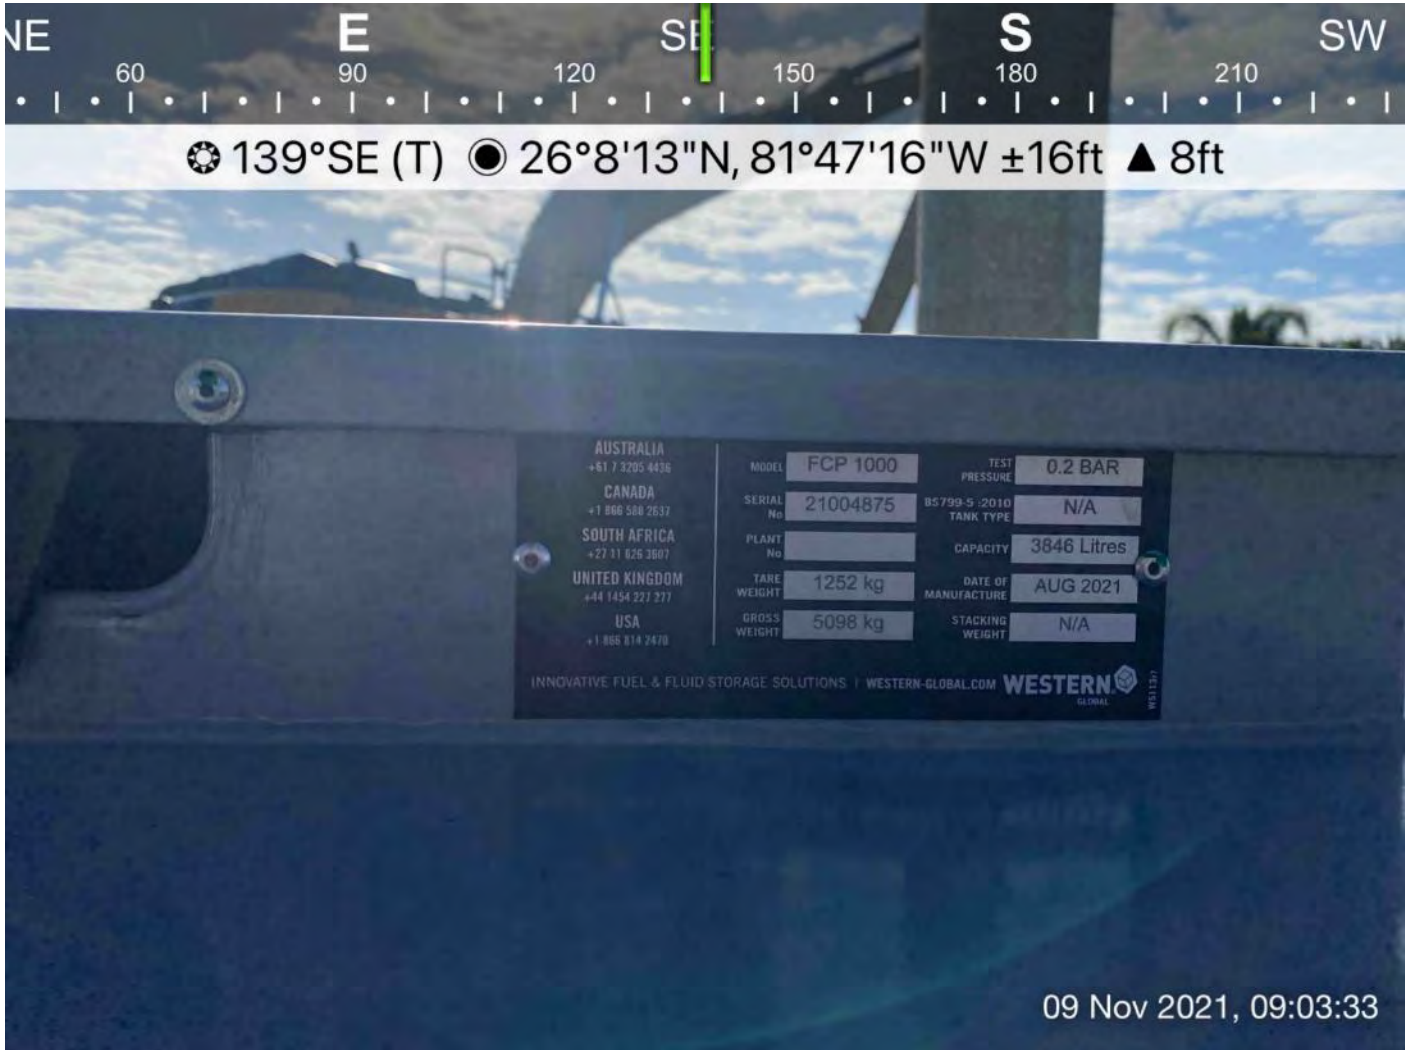

Large fuel cube ID information

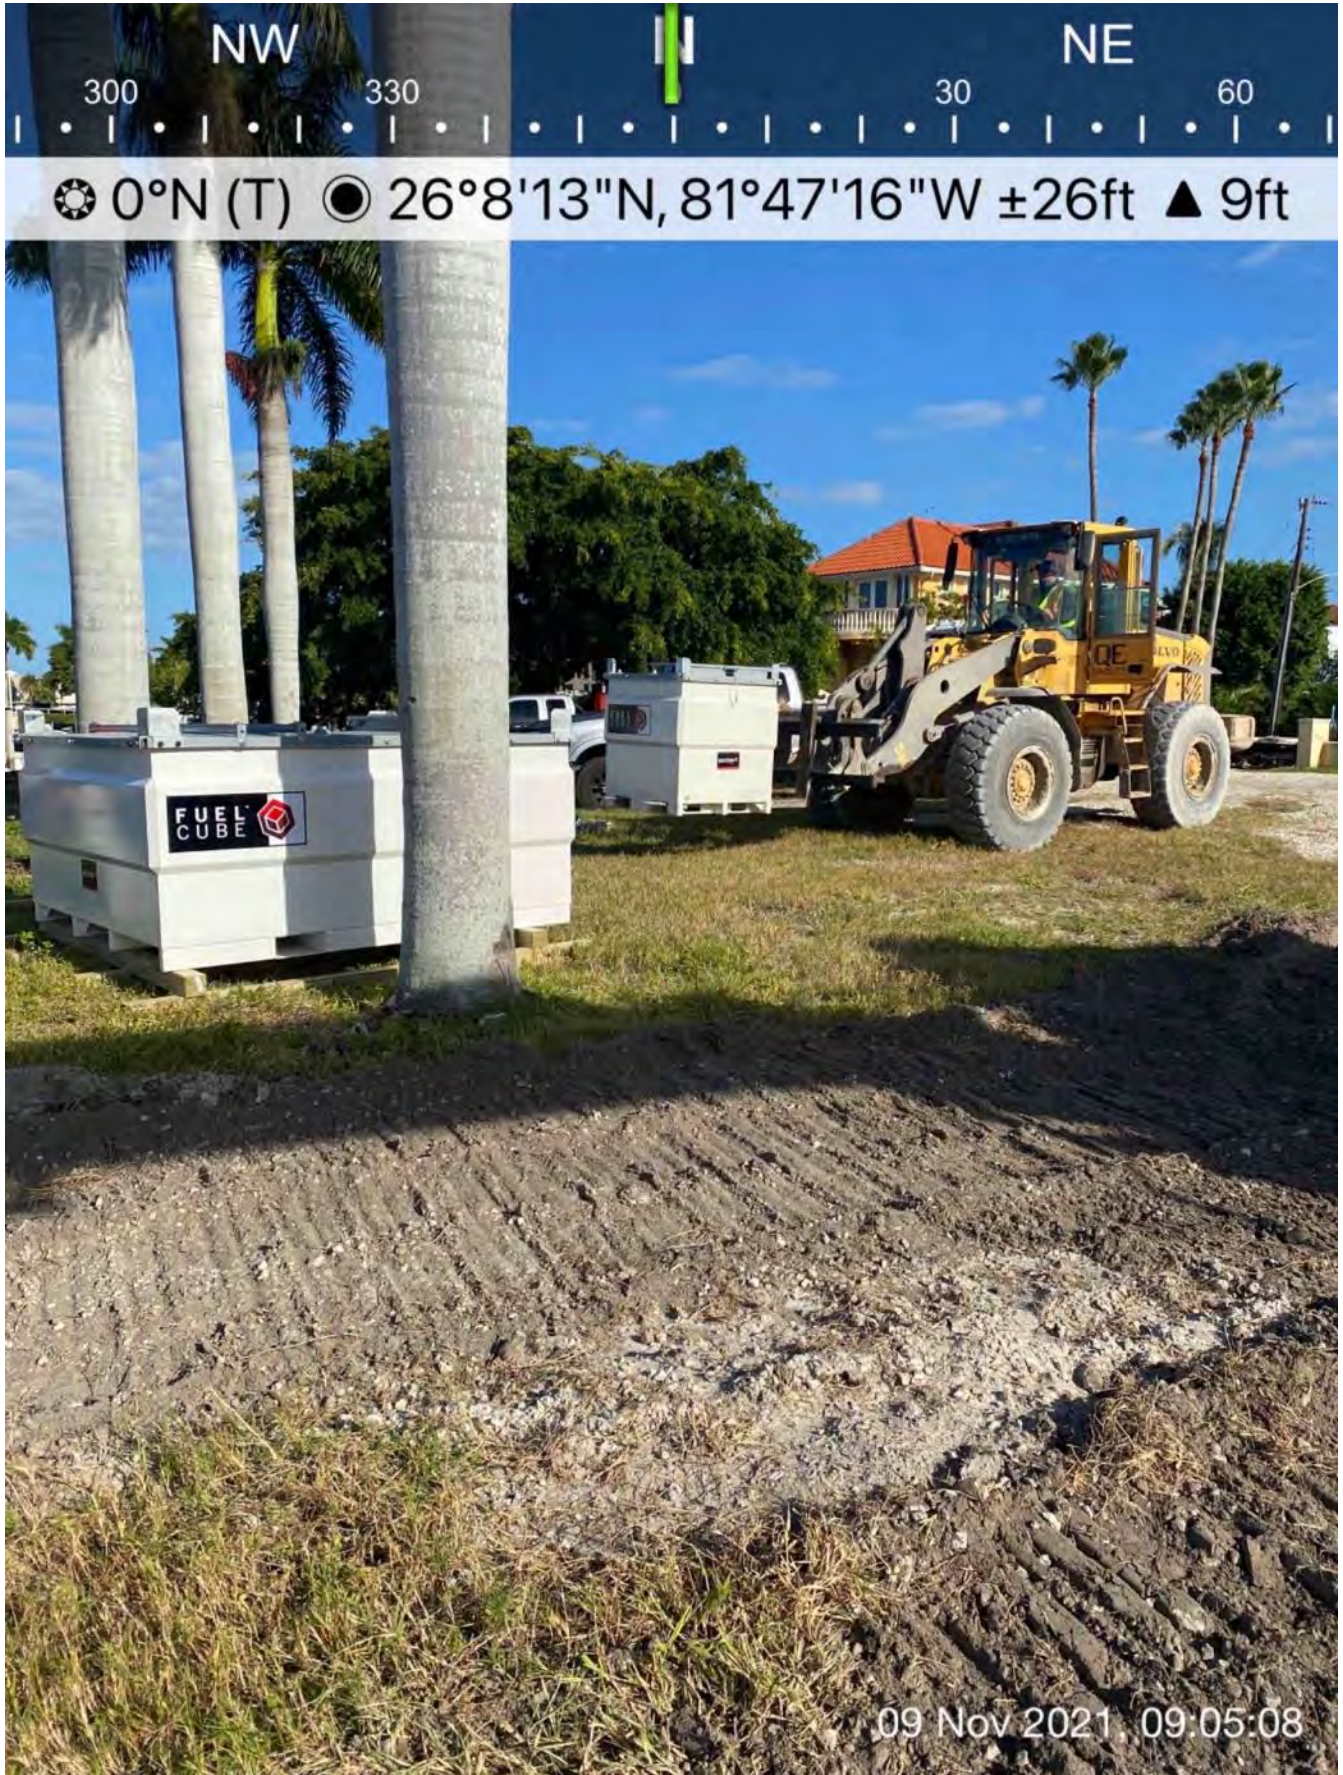

Front end loader moving large fuel cube from transport truck to empty lot at 1300 Curlew Avenue

E 90 SE 180 S
60 90 120 150 180
☉ 129°SE (T) ☉ 26°8'13"N, 81°47'15"W ±39ft ▲ 8ft



09 Nov 2021, 10:31:50

323 excavator grinding rock in Canal CC-CC at station 2+50

W NW N
240 270 300 330 0
☀ 308°NW (T) ☉ 26°8'13"N, 81°47'15"W ±26ft ▲ 7ft



326 excavator towing dump truck

SE S SW
120 150 180 210 240

☀ 185°S (T) ● 26°8'14"N, 81°47'16"W ±32ft ▲ 8ft




Fuel truck filing up both fuel cubes



☀ 164°S (T) ● 26°8'13"N, 81°47'15"W ±29ft ▲ 8ft



323 excavator lifting spud to allow push boat to move the barge

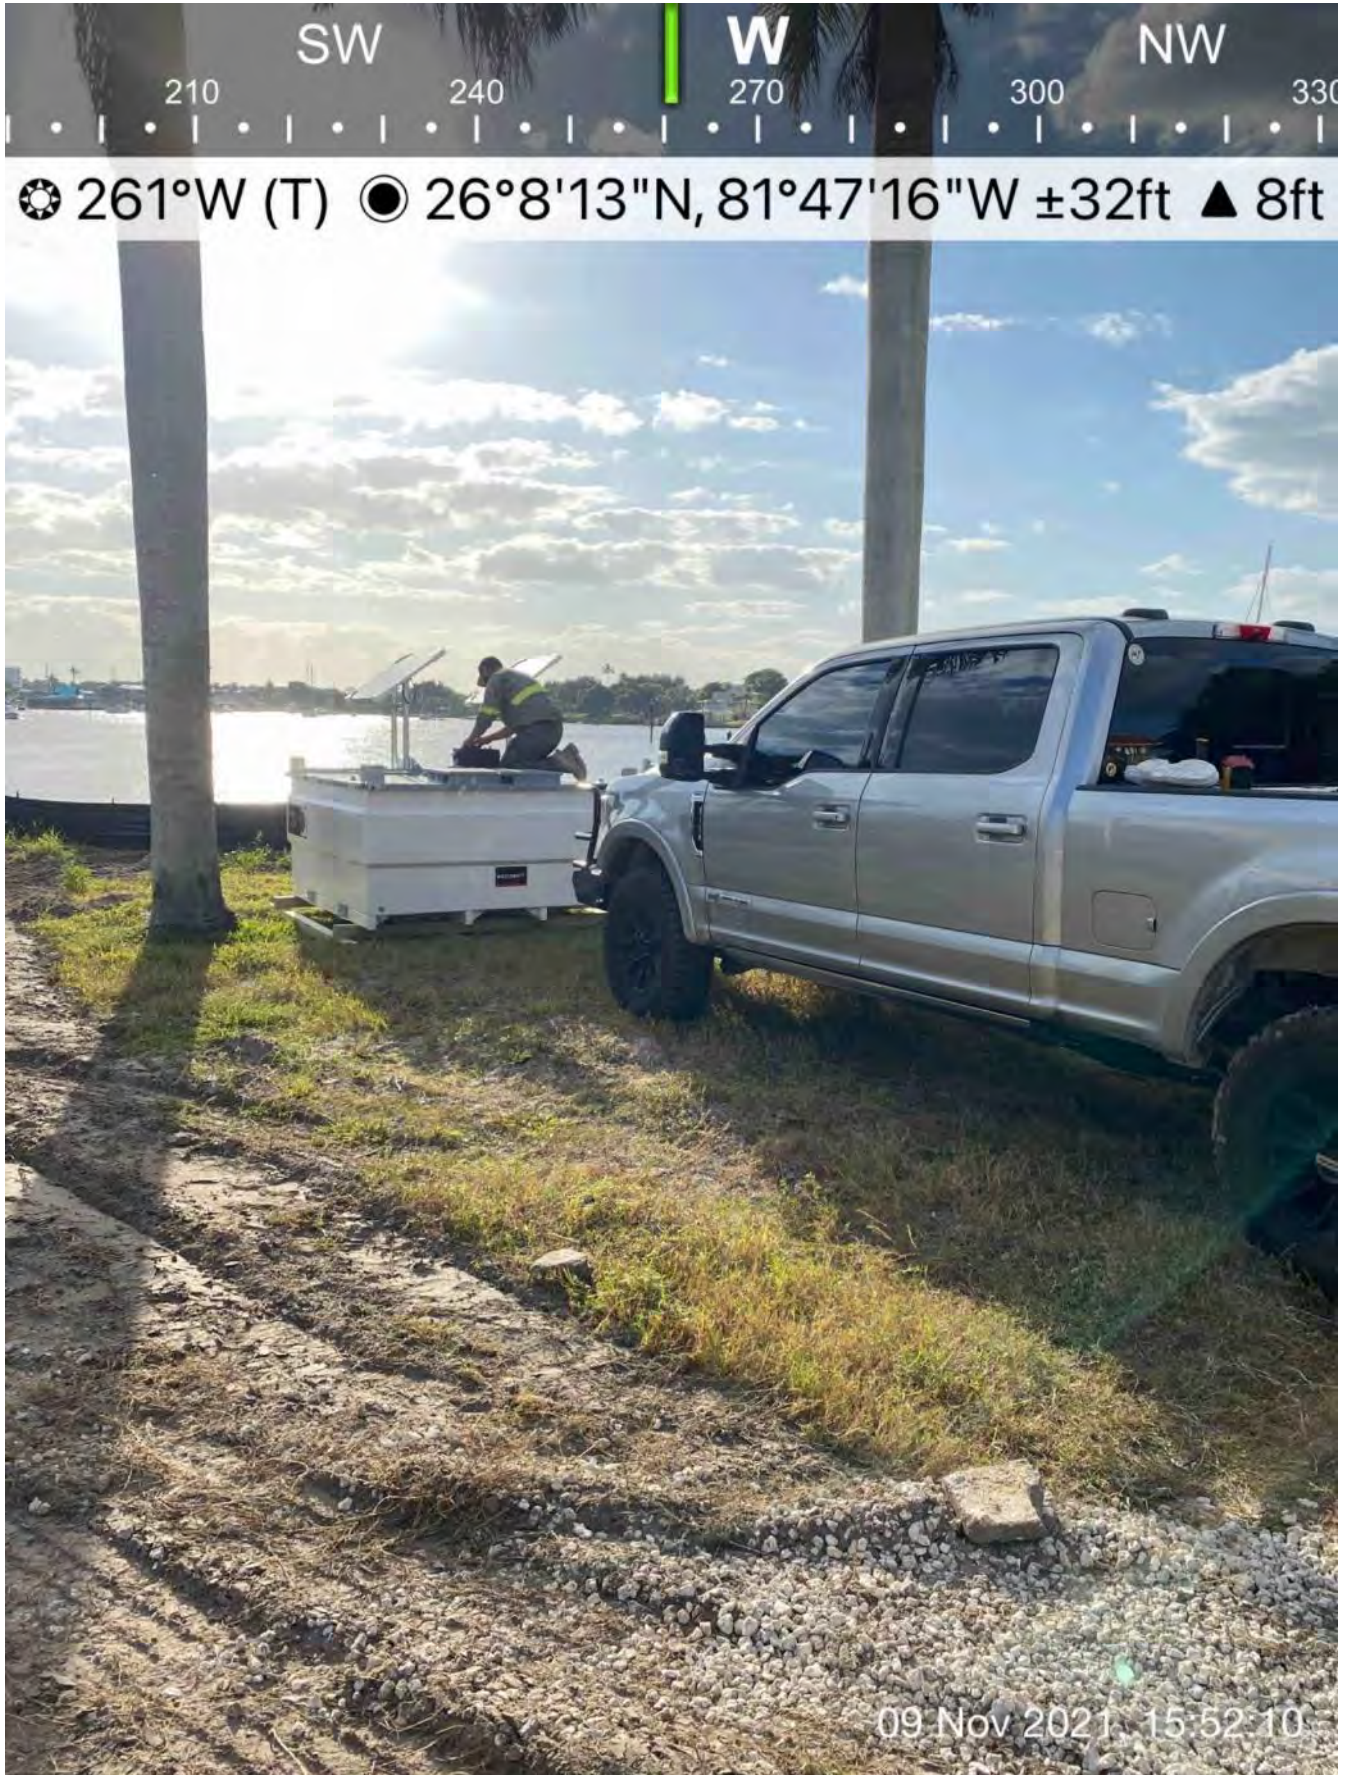

Setting up solar panels for the battery on the large fuel cube

E SE S
60 90 120 150 180
☀ 124°SE (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 8ft



323 excavator grinding rock at station 2+50 and 326 excavator holding barge in place



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 11/10/2021			
Inspectors: SB	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Wednesday	Contract Day: 24/365	Week: 4	Accident Report #: N/A
High Temp (°F): 80°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 7:07 PM – +2.3'
Low Temp (°F): 64°F	Wind: 8mph	Wind: 9mph	Low Tide: 11:49 AM – -0.1'
Canal Worked In: CC-CC	Stations Worked Between:	1+00 to 3+00	

General

#1 – Prime Contractor – Quality Enterprises:

- Contractor’s equipment is staged in canal CC-CC towards the west end of the canal (between stations 2+00 and 2+50). This equipment includes an excavator mounted on the barge, a hopper, a push boat, and a support boat. Contractor also has two other excavators, two fuel cubes, and a water truck staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor installed turbidity curtain across mouth of Canal CC-CC.
- Contractor grinded rock with the 323 excavator at station 3+00 from 8:00 am to 8:45 am.
- Utility truck and technician came at 9:00 am.
- Contractor used the small fuel cube to fill the 326 excavator and the front end loader with fuel.
- Contractor used 326 excavator to transport small fuel cube from the south side of the empty lot at 1300 Curlew Avenue to the push boat.
- Contractor used push boat to transport small fuel cube to the barge so that 323 excavator could fill its tank.
- Push boat was used to transport small fuel cube within reach of the 326 excavator which then moved it back to its location at the south side of the empty lot at 1300 Curlew Avenue.
- Contractor used the 323 excavator to grind rock at station 2+50 from 10:00 am to 12:00 pm.
- Contractor resumed grinding rock between stations 2+50 and 3+00 from 1:15 pm to 5:00 pm.
- Contractor finished work for the day and left the barge, excavator, support boat, push boat, and hopper in canal CC-CC near station 3+00. The contractor left the 326 excavator, the front end loader, the water truck, and the two fuel cubes on the empty lot.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	1	0.75	Boat Captain	1	9	Foreman	0	0
		Excavator Operator	1	9	Truck Driver	0	0	Assistant	1	9
		Technician	1	2	Superintendent	1	9	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	9
1	CAT 326	Excavator	1	1	1
1	02016	Front End Loader	1	1	0.25
1	FL6223TB	Push Boat	1	1	5
1	FL2474PP	Support Boat	1	1	2
1	N6143X	Fuel Truck	1	0	0
1	P9457E	Water Truck	1	0	0
1	Z67EAZ	Dump truck	1	0	0
1	MB38DQ	Utility Truck	1	1	2
1	5178CR	Transport Truck	1	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:
Jack Hooper	Quality Enterprises	8:00 AM	8:45 AM

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT – Inspector	From: 8:00 AM	To: 5:00 PM	9 hours

N 0 30 NE 60 E 90
☀ 47°NE (T) ☉ 26°8'13"N, 81°47'16"W ±32ft ▲ 8ft



Technician connecting jumper cables from car battery to fuel cell battery. Assistant filling up 326 excavator with fuel.

E 90 SE 120 150 S 180 210

☉ 141°SE (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 9ft



326 excavator transporting small fuel cell from south side of empty lot at 1300 Curlew Avenue to push boat



☀ 101°E (T) ☉ 26°8'13"N, 81°47'16"W ±36ft ▲ 8ft



326 excavator transporting small fuel cell from south side of empty lot at 1300 Curlew Avenue to push boat

E 90 SE 120 150 S 180
☀ 131°SE (T) ☉ 26°8'13"N, 81°47'16"W ±55ft ▲ 8ft



Push boat moving barge and hopper tied to barrier walls on the North side of Canal CC-CC near station 1+50



☀ 207°SW (T) ● 26°8'13"N, 81°47'14"W ±22ft ▲ 8ft



323 excavator grinding rock at station 2+50

SE S SW
120 150 180 210
☀ 165°S (T) ● 26°8'13"N, 81°47'14"W ±29ft ▲ 8ft



10 Nov 2021, 16:55:26

323 excavator grinding rock at station 2+50



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 11/11/2021			
Inspectors: SB	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Thursday	Contract Day: 25/365	Week: 4	Accident Report #: N/A
High Temp (°F): 81°F	AM Conditions: Partly-Cloudy Wind: 6mph	PM Conditions: Partly-Cloudy Wind: 7mph	High Tide: 5:39 AM – +2.6'
Low Temp (°F): 67°F			Low Tide: 12:59 PM – +0.3'
Canal Worked In: CC-CC	Stations Worked Between:	1+50 to 3+00	

General
<p>#1 – Prime Contractor – Quality Enterprises:</p> <ul style="list-style-type: none"> Contractor’s equipment is staged in canal CC-CC towards the west end of the canal (between stations 2+00 and 2+50). This equipment includes an excavator mounted on the barge, a hopper, and a push boat. Contractor also has two other excavators, two fuel cubes, and a water truck staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102. Contractor installed turbidity curtain across the mouth of Canal CC-CC. Contractor grinded rock with the 323 excavator at station 3+00 from 8:30 am to 12:00 pm. Contractor brought the support boat to the empty lot at 1300 Curlew Avenue by truck and left it staged on land. Contractor removed turbidity curtain from mouth of Canal CC-CC to let another contractor with a barge, crane, and excavator enter the canal. Contractor re-installed turbidity curtain after other contractor had entered Canal CC-CC. Contractor inspected the Epiroc grinder for signs of damage and removed the grinder from the 323 excavator and used the front end loader to place it on the southwest corner of the empty lot at 1300 Curlew Avenue. Contractor put the bucket on the 323 excavator and removed rock and sediment from station 3+00 and placed the sediment into the hopper. Push boat moved the hopper to the edge of the empty lot at 1300 Curlew Avenue. Contractor transferred dredged material from the hopper to the dewatering site on the empty lot at 1300 Curlew Avenue. Utility truck came to the empty lot at 1300 Curlew Avenue at 3:30 pm. Contractor finished work for the day and left the barge, 323 excavator, support boat, and hopper in canal CC-CC near station 2+00. The contractor left the 326 excavator, the front end loader, the water truck, the support boat, and the two fuel cubes on the empty lot.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	1	1	Boat Captain	1	9	Foreman	0	0
		Excavator Operator	1	9	Truck Driver	1	1	Assistant	1	9
		Technician	1	1	Superintendent	1	9	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	7
1	CAT 326	Excavator	1	1	1
1	02016	Front End Loader	1	1	0.25
1	FL6223TB	Push Boat	1	1	5
1	FL2474PP	Support Boat	1	1	0
1	N6143X	Fuel Truck	1	0	0
1	P9457E	Water Truck	1	0	0
1	Z67EAZ	Dump truck	1	0	0
1	MB38DQ	Utility Truck	1	1	1
1	5178CR	Transport Truck	1	0	0


Visitors			
Name	Company	Hours at Job Site	
		From:	To:
Jack Hooper	Quality Enterprises	8:30 AM	9:00 AM
Jack Hooper	Quality Enterprises	1:15 PM	1:45 PM

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT – Inspector	From: 8:30 AM	To: 4:30 PM	8 hours

N 0 30 NE 60 E 90 1
☉ 48°NE (T) ☉ 26°8'14"N, 81°47'16"W ±26ft ▲ 8ft



Water truck and front end loader as they were staged overnight from 11/10 to 11/11 at 1300 Curlew Avenue

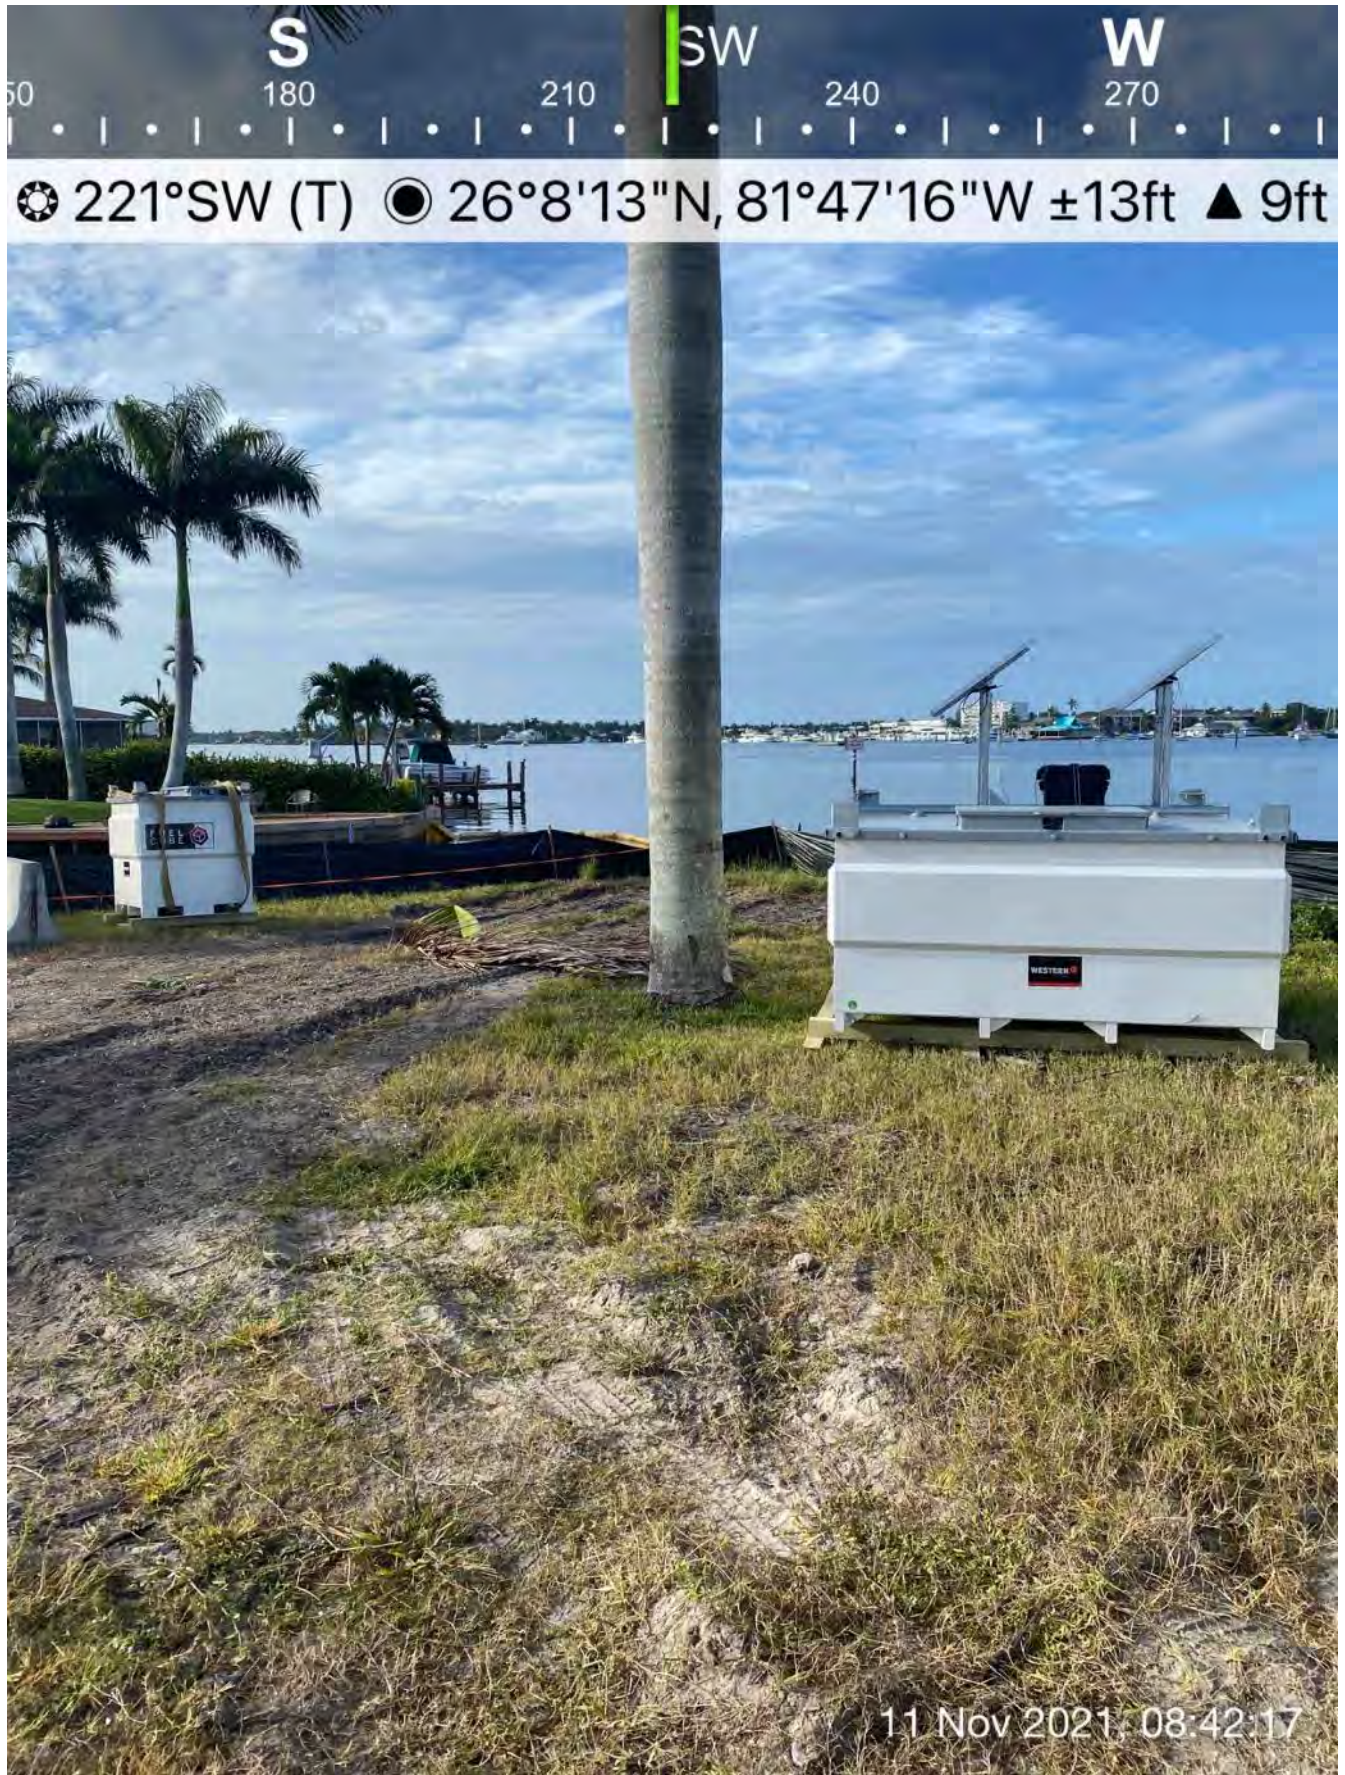

Large and small fuel cube as they were staged overnight from 11/10 to 11/11 at 1300 Curlew Avenue



☀ 190°S (T) ● 26°8'13"N, 81°47'16"W ±13ft ▲ 8ft



11 Nov 2021, 08:42:45

Turbidity curtain across the mouth of Canal CC-CC

S SW W
150 180 210 240 270

☉ 215°SW (T) ● 26°8'12"N, 81°47'14"W ±32ft ▲ 8ft



323 excavator grinding rock at station 3+00

S 180 SW W 270
50 180 210 240 270

☉ 221°SW (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 10ft



Another contractor's barge, crane, and push boat entering Canal CC-CC

E SE S
60 90 120 150 180
127°SE (T) 26°8'13"N, 81°47'16"W ±13ft ▲ 8ft



Another contractor's barge, crane, and push boat moving west down canal CC-CC



Another contractor's barge, crane, and push boat near a dock at station 4+00

E 90 SE 120 180 S 210

☉ 150°SE (T) ● 26°8'13"N, 81°47'15"W ±32ft ▲ 8ft



Inspecting Epiroc grinder attached to 323 excavator

S 180 SW 210 W 270

☉ 225°SW (T) ● 26°8'13"N, 81°47'15"W ±39ft ▲ 7ft



Inspecting Epiroc grinder attached to 323 excavator



☀ 76°E (T) ● 26°8'13"N, 81°47'15"W ±72ft ▲ 8ft



Front end loader transporting Epiroc grinder to the empty lot at 1300 Curlew Avenue



☀ 10°N (T) ☉ 26°8'13"N, 81°47'16"W ±65ft ▲ 8ft



11 Nov 2021, 14:02:41

Front end loader transporting Epiroc grinder to the empty lot at 1300 Curlew Avenue

SE 120 150 180 210 SW

☀ 167°S (T) ● 26°8'13"N, 81°47'15"W ±39ft ▲ 8ft



11 Nov 2021, 14:53:24

323 excavator transporting rock and sediment from station 3+00 to hopper



323 excavator transporting rock and sediment from station 3+00 to hopper


W NW N
240 270 300 330 0

☉ 304°NW (T) ● 26°8'13"N, 81°47'15"W ±16ft ▲ 8ft



11 Nov 2021, 15:26:17

326 excavator transporting rock and sediment from the hopper to the dewatering site at 1300 Curlew Avenue



☉ 114°SE (T) ● 26°8'13"N, 81°47'16"W ±22ft ▲ 7ft



326 excavator transporting rock and sediment from the hopper to the dewatering site at 1300 Curlew Avenue



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 11/12/2021			
Inspectors: SB	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Friday	Contract Day: 26/365	Week: 4	Accident Report #: N/A
High Temp (°F): 81°F	AM Conditions: Cloudy	PM Conditions: Cloudy	High Tide: 7:13 AM – +2.5'
Low Temp (°F): 71°F	Wind: 1mph	Wind: 6mph	Low Tide: 2:04 PM – +0.5'
Canal Worked In: CC-CC	Stations Worked Between:	1+50 to 2+00	

General	
#1 – Prime Contractor – Quality Enterprises:	
<ul style="list-style-type: none"> Contractor’s equipment is staged in canal CC-CC towards the west end of the canal (between stations 1+50 and 2+00). This equipment includes an excavator mounted on the barge, a hopper, and a push boat. Contractor also has two other excavators, two fuel cubes, a support boat, and a water truck staged on the empty lot property located at 1300 Curlew Avenue, Naples, FL, 34102. Collier Seawall and Dock’s barge and push boat passed contractor’s equipment staged between stations 1+50 and 2+00 as it exited Canal CC-CC at 8:00 am Contractor inspected and greased the 323 excavator and the 326 excavator. Contractor cleaned the 323 excavator, 326 excavator, hopper, and push boat with water from the water truck. Contractor finished work for the day at 9:30 am and left the barge, 323 excavator, push boat, and hopper in canal CC-CC between stations 1+50 and 2+00. The contractor left the 326 excavator, the front end loader, the water truck, the support boat, and the two fuel cubes on the empty lot. 	

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	0	0	Foreman	0	0
		Excavator Operator	1	2	Truck Driver	0	0	Assistant	1	2
		Technician	0	0	Superintendent	1	2	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	1
1	CAT 323	Excavator	1	1	1
1	CAT 326	Excavator	1	1	1
1	02016	Front End Loader	1	0	0
1	FL6223TB	Push Boat	1	0	5
1	FL2474PP	Support Boat	1	0	0
1	N6143X	Fuel Truck	1	0	0
1	P9457E	Water Truck	1	1	1
1	Z67EAZ	Dump truck	1	0	0
1	MB38DQ	Utility Truck	1	0	0
1	5178CR	Transport Truck	1	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT – Inspector	From: 8:00 AM	To: 10:00 PM	2 hours




☉ 122°SE (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 15ft



12 Nov 2021, 08:10:30

Collier Seawall and Dock boat and barge passing contractor's staged equipment while exiting Canal CC-CC



☉ 138°SE (T) ● 26°8'13"N, 81°47'16"W ±19ft ▲ 8ft



12 Nov 2021, 08:11:35

Collier Seawall and Dock boat and barge passing contractor's staged equipment while exiting Canal CC-CC



Epiroc grinder on the empty lot at 1300 Curlew Avenue

E 90 SE 120 150 S 180
☉ 128°SE (T) ☉ 26°8'13"N, 81°47'15"W ±45ft ▲ 8ft



12 Nov 2021, 08:16:48

Inspecting, greasing, and cleaning the 323 excavator

W 270 NW 300 330 N 0 NE 30

☀ 338°NW (T) ☉ 26°8'13"N, 81°47'16"W ±49ft ▲ 8ft



Inspecting, greasing, and cleaning the 326 excavator



326 excavator, Epiroc grinder, and two fuel cubes staged in the southwest corner of the lot at 1300 Curlew Avenue



☀ 45°NE (T) ● 26°8'13"N, 81°47'16"W ±13ft ▲ 9ft



12 Nov 2021, 09:19:53

Water truck, front end loader, and support boat staged on the east side of the lot at 1300 Curlew Avenue



☀ 137°SE (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 11ft



Barge, 323 excavator, push boat, and hopper staged in Canal CC-CC between stations 1+50 and 2+00
