



WEEKLY SUMMARY REPORT – CONTRACT WEEK 25

21-036 EAST NAPLES BAY

DREDGING AND ROCK REMOVAL PROJECT



Date: 4/4/2022 to 4/8/2022			
Inspectors: Sam Boyd	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Days of Week: Monday to Friday	Contract Days: 169 to 173	Total Days: 365	Accident Report #: N/A
Canal(s) Worked In: BB-BB / CC-CC		Stations Worked Between: 0+00 to 9+00 / 1+00 to 14+50	

General

Remarks

#1 – Prime Contractor – Quality Enterprises:

Monday 04-04-2022:

- Contractor has an excavator mounted on a barge staged in Canal CC-CC at station 1+00. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC at station 1+50. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor used 326 excavator to redistribute removed material at the dewatering site at 1300 Curlew Avenue.
- Contractor used push boat to transport barge, 323 excavator, and hopper from Canal CC-CC to Canal BB-BB.
- Contractor installed turbidity curtain across the mouth of Canal BB-BB.
- Fuel truck came on site at 1300 Curlew Avenue and refilled the fuel cubes.
- Contractor used 323 excavator to remove 3 hoppers of material between stations 6+00 and 9+00.
- Contractor used push boat to position barge as necessary for removing material, as well as for transferring hoppers between Canal BB-BB and Canal CC-CC.
- Contractor used 326 excavator to transfer 3 hoppers of material from hopper to dewatering site at 1300 Curlew Avenue.

Tuesday 04-05-2022:

- Contractor has an excavator mounted on a barge staged in Canal BB-BB at station 6+00. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC at station 1+50. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor used 326 excavator to redistribute removed material at the dewatering site at 1300 Curlew Avenue.
- Contractor used 326 excavator to transfer removed material from the dewatering site to the dump truck.
- 6 truckloads of material were taken off the site at 1300 Curlew Avenue by dump trucks.
- Contractor installed turbidity curtain across the mouth of Canal BB-BB.
- Contractor used 323 excavator to remove 4.5 hoppers of material between stations 2+00 and 5+50.
- Contractor used push boat to position barge as necessary for removing material, as well as for transferring hoppers between Canal BB-BB and Canal CC-CC.
- Mechanic came to site to fix 326 excavator.



WEEKLY SUMMARY REPORT – CONTRACT WEEK 25

21-036 EAST NAPLES BAY

DREDGING AND ROCK REMOVAL PROJECT



- Contractor used 326 excavator to transfer 4.5 hoppers of material from hopper to dewatering site at 1300 Curlew Avenue.

Wednesday 04-06-2022:

- Contractor has an excavator mounted on a barge staged in Canal BB-BB at station 0+50. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC at station 1+50. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor installed turbidity curtain across the mouth of Canal BB-BB.
- Contractor used 323 excavator to check elevations and remove material between stations 0+00 and 0+50.
- Contractor used push boat to transport barge, 323 excavator, and hopper back to Canal CC-CC.
- Contractor used 326 excavator to redistribute removed material at the dewatering site at 1300 Curlew Avenue.
- Contractor used 326 excavator to transfer removed material from the dewatering site to the dump truck.
- 15 truckloads of material were taken off the site at 1300 Curlew Avenue by dump trucks.
- Contractor installed turbidity curtain across the mouth of Canal CC-CC.
- Contractor used 323 excavator to remove 1 hopper of material between stations 2+00 and 14+50.
- Contractor used push boat to position barge as necessary for removing material.
- Contractor used 326 excavator to transfer 1 hopper of material from hopper to dewatering site at 1300 Curlew Avenue.

Thursday 04-07-2022:

- Contractor has an excavator mounted on a barge staged in Canal CC-CC at station 1+50. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC at station 2+00. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor waited to let Police boat resident out of Canal CC-CC before attaching curtain or mobilizing barge.
- Contractor installed turbidity curtain across the mouth of Canal CC-CC.
- Contractor used 323 excavator to check elevations and remove material between stations 1+50 and 3+50.
- Contractor used push boat to position barge as necessary for removing material as well as to open and close the turbidity curtain to let another resident exit Canal CC-CC.
- Contractor used push boat to transport 323 excavator, barge, and hopper out to the bay to allow Morgan and Eklund survey boat access.
- Contractor used push boat to transport 323 excavator, barge, and hopper back to Canal CC-CC station 1+50.
- Contractor used front end loader to redistribute removed material at the dewatering site at 1300 Curlew Avenue.
- Contractor used 326 excavator to transfer removed material from the dewatering site to the dump truck.



WEEKLY SUMMARY REPORT – CONTRACT WEEK 25
21-036 EAST NAPLES BAY
DREDGING AND ROCK REMOVAL PROJECT



- 8 truckloads of material were taken off the site at 1300 Curlew Avenue by dump trucks.

Friday 04-08-2022:

- Contractor has an excavator mounted on a barge staged in Canal CC-CC at station 1+00. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor pumped water out from the bottom of the barge.
- Contractor greased 323 and 326 excavators and refilled with DEF.
- Contractor filled water tank with fire hydrant outside of 1300 Curlew Avenue.
- Contractor used water tank to clean all equipment on site and stationed in Canal CC-CC.

Note: Daily reports with pictures attached for the week.



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 04/04/2022			
Inspectors: SB	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Monday	Contract Day: 169/365	Week: 25	Accident Report #: N/A
High Temp (°F): 86°F	AM Conditions: Cloudy	PM Conditions: Cloudy	High Tide: 3:04 PM +2.6'
Low Temp (°F): 67°F	Wind: 8 mph	Wind: 17 mph	Low Tide: 9:46 AM +0.9'
Canal Worked In: BB-BB	Stations Worked Between:	6+00 to 9+00	

General	
#1 – Prime Contractor – Quality Enterprises:	
<ul style="list-style-type: none"> • Contractor has an excavator mounted on a barge staged in Canal CC-CC at station 1+00. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC at station 1+50. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102. • Contractor used 326 excavator to redistribute removed material at the dewatering site at 1300 Curlew Avenue. • Contractor used push boat to transport barge, 323 excavator, and hopper from Canal CC-CC to Canal BB-BB. • Contractor installed turbidity curtain across the mouth of Canal BB-BB. • Fuel truck came on site at 1300 Curlew Avenue and refilled the fuel cubes. • Contractor used 323 excavator to remove 3 hoppers of material between stations 6+00 and 9+00. • Contractor used push boat to position barge as necessary for removing material, as well as for transferring hoppers between Canal BB-BB and Canal CC-CC. • Contractor used 326 excavator to transfer 3 hoppers of material from hopper to dewatering site at 1300 Curlew Avenue. 	

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	1	9	Mechanic	1	2
		Excavator Operator	2	9	Truck Driver	0	0	Assistant	1	9
		Technician	0	0	Superintendent	1	3	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	9
1	CAT 326	Excavator	1	1	5
1	02016	Front End Loader	1	0	0
1	FL6223TB	Push Boat	1	1	8
1	FL2474PP	Support Boat	1	0	0
1	N3758Z	Fuel Truck	1	1	2
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	0	0	0
1	MB28DQ	Dump truck	0	0	0
1	MB26DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:30 AM	To: 4:30 PM	8.0



☀ 177°S (T) ☉ 26°8'15"N, 81°47'15"W ±29ft ▲ 8ft



326 excavator redistributing removed material at the dewatering site at 1300 Curlew Avenue

SW W NW
210 240 270 300 330
☉ 262°W (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 7ft



Push boat transporting barge and 323 excavator from Canal CC-CC to Canal BB-BB



☀ 357°N (T) ☉ 26°8'8"N, 81°47'7"W ±39ft ▲ 8ft



323 excavator lifting spud to allow push boat to mobilize barge at station 9+00



☉ 5°N (T) ☉ 26°8'8"N, 81°47'7"W ±13ft ▲ 6ft



04 Apr 2022, 10:02:58

323 excavator removing material from station 9+00

W 270 NW 300 330 N 0 NE 30
☀ 338°N (T) ☉ 26°8'8"N, 81°47'16"W ±42ft ▲ 126ft



Turbidity curtain across the mouth of Canal BB-BB

S 180 SW 210 240 W 270 NW 300
☀ 247°SW (T) ☉ 26°8'13"N, 81°47'15"W ±26ft ▲ 9ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue




Mechanic truck refilling the fuel cubes at 1300 Curlew Avenue

E 90 SE 120 150 S 180 SW 210

☀ 157°SE (T) ● 26°8'14"N, 81°47'16"W ±16ft ▲ 8ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue




☉ 43°NE (T) ☉ 26°8'9"N, 81°47'9"W ±13ft ▲ 9ft



04 Apr 2022, 13:42:53

323 excavator removing material from station 6+50

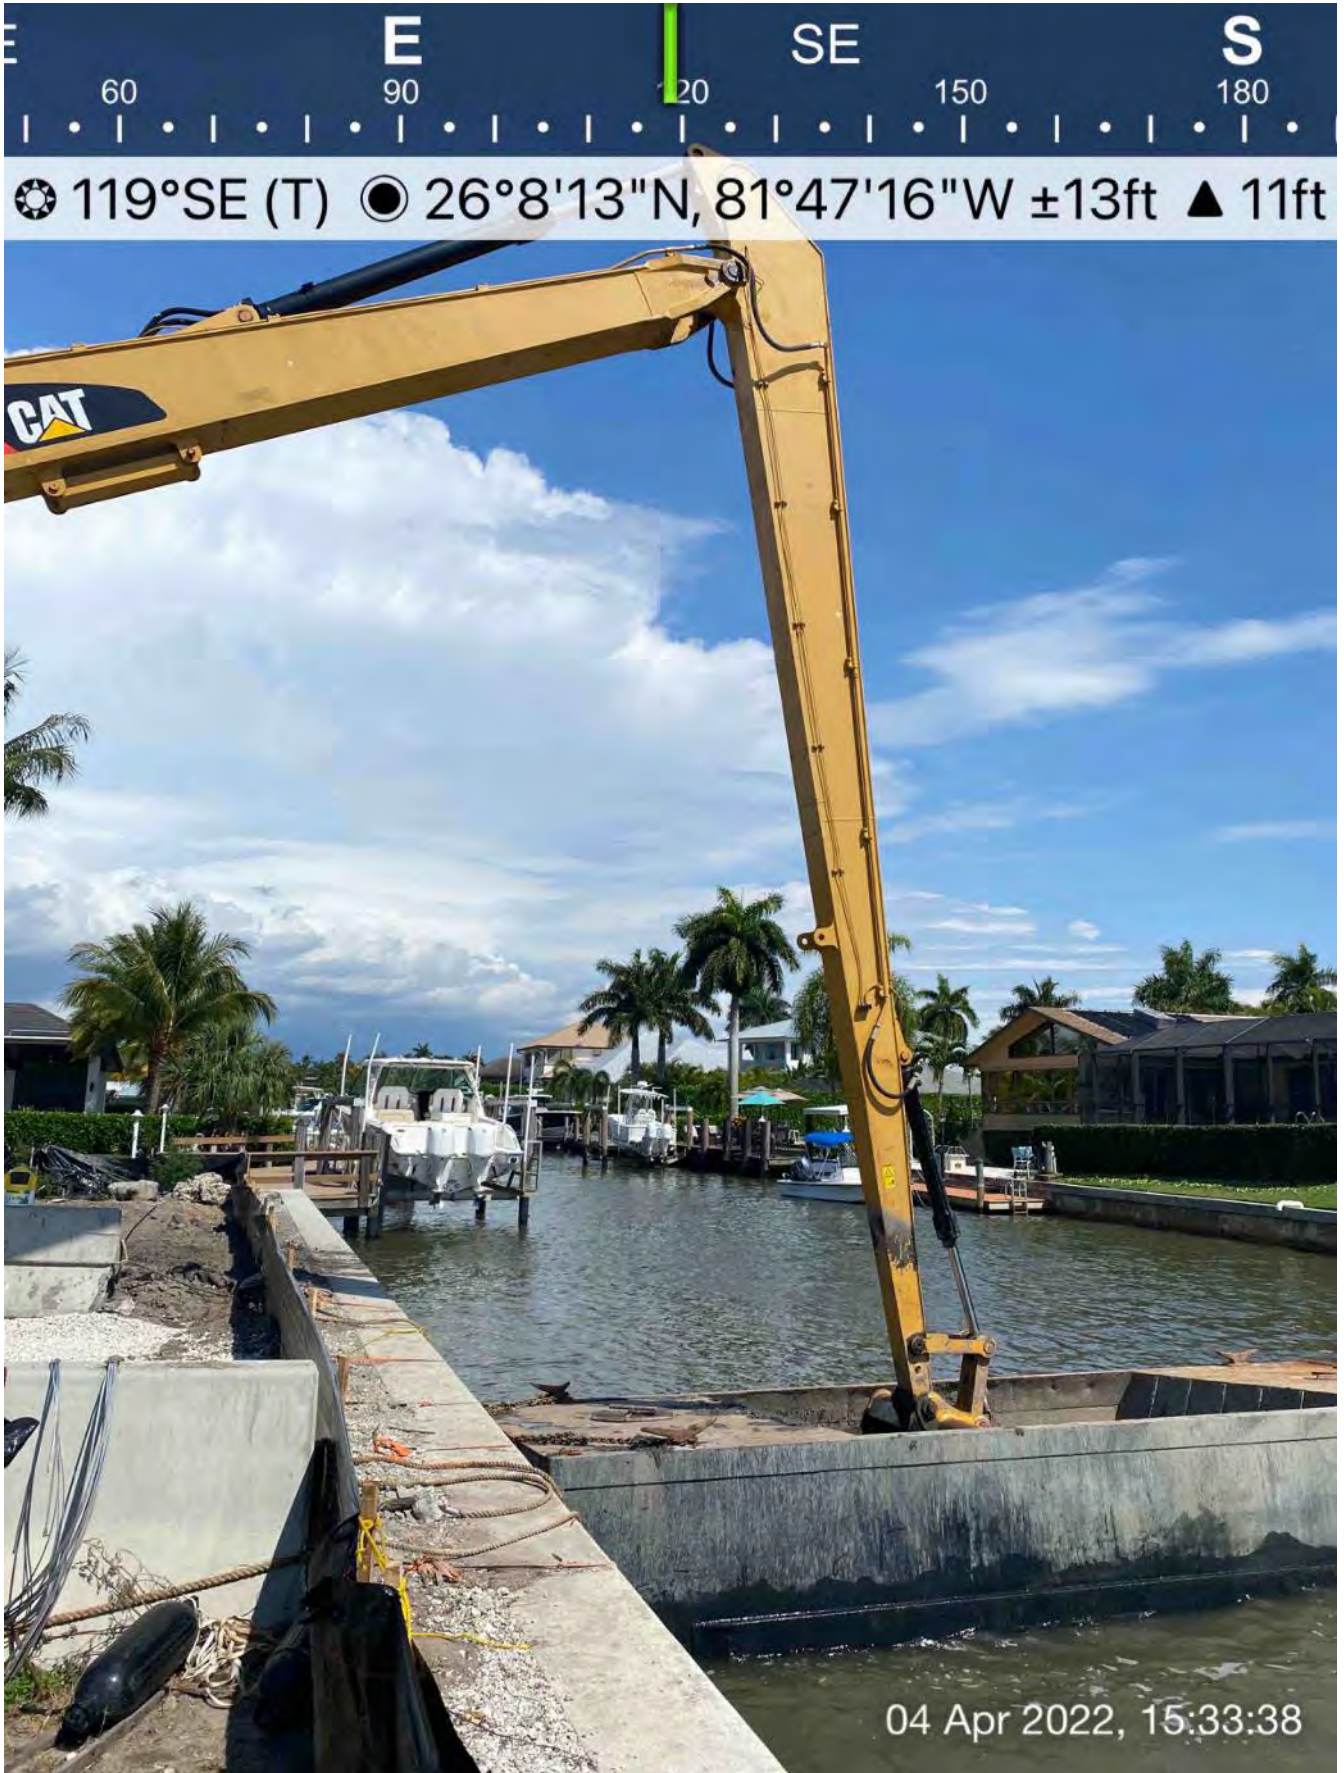

326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue

W 270 NW 300 N 0 30

☉ 320°NW (T) ☉ 26°8'8"N, 81°47'10"W ±114ft ▲ 9ft



04 Apr 2022, 16:12:51

323 excavator removing material from station 6+00



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 04/05/2022			
Inspectors: SB	Stantec PIN: 2028113191	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: Tuesday	Contract Day: 170/365	Week: 25	Accident Report #: N/A
High Temp (°F): 89°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 3:29 PM +2.5'
Low Temp (°F): 67°F	Wind: 11 mph	Wind: 19 mph	Low Tide: 10:08 AM +1.1'
Canal Worked In: BB-BB	Stations Worked Between:	2+00 to 5+50	

General	
#1 – Prime Contractor – Quality Enterprises:	
<ul style="list-style-type: none"> • Contractor has an excavator mounted on a barge staged in Canal BB-BB at station 6+00. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC at station 1+50. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102. • Contractor used 326 excavator to redistribute removed material at the dewatering site at 1300 Curlew Avenue. • Contractor used 326 excavator to transfer removed material from the dewatering site to the dump truck. • 6 truckloads of material were taken off the site at 1300 Curlew Avenue by dump trucks. • Contractor installed turbidity curtain across the mouth of Canal BB-BB. • Contractor used 323 excavator to remove 4.5 hoppers of material between stations 2+00 and 5+50. • Contractor used push boat to position barge as necessary for removing material, as well as for transferring hoppers between Canal BB-BB and Canal CC-CC. • Mechanic came to site to fix 326 excavator. • Contractor used 326 excavator to transfer 4.5 hoppers of material from hopper to dewatering site at 1300 Curlew Avenue. 	

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	1	9	Mechanic	1	2
		Excavator Operator	2	9	Truck Driver	2	8	Assistant	1	9
		Technician	0	0	Superintendent	1	3	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	9
1	CAT 326	Excavator	1	1	5
1	02016	Front End Loader	1	0	0
1	FL6223TB	Push Boat	1	1	8
1	FL2474PP	Support Boat	1	0	0
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	0	0	0
1	MB28DQ	Dump truck	0	0	0
1	MB26DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	1	1	2
1	N9524Z	Transport Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 9:30 AM	To: 5:30 PM	8.0



☉ 232°SW (T) ☉ 26°8'15"N, 81°47'15"W ±22ft ▲ 8ft




326 excavator transferring removed material from dewatering site to dump truck bed at 1300 Curlew Avenue

W 270 NW 300 N 330 0

☀ 314°NW (T) ● 26°8'8"N, 81°47'12"W ±13ft ▲ 9ft



323 excavator removing material and transferring to hopper at station 4+50



☀ 38°NE (T) ☉ 26°8'8"N, 81°47'13"W ±13ft ▲ 7ft



323 excavator lifting spud to allow push boat to mobilize barge at station 4+50




☀ 327°NW (T) ● 26°8'8"N, 81°47'16"W ±22ft ▲ 8ft



05 Apr 2022, 10:27:24

Push boat opening turbidity curtain from across the mouth of Canal BB-BB



☀ 35°NE (T) ● 26°8'8"N, 81°47'13"W ±13ft ▲ 8ft



05 Apr 2022, 11:40:02

323 excavator removing material from station 4+00

SE 150 S 180 SW 210 240
☀ 195°S (T) ☉ 26°8'14"N, 81°47'16"W ±19ft ▲ 9ft



Mechanic on site at 1300 Curlew Avenue to fix 326 excavator

SW 240 W 270 NW 330 N 0
● 294°NW (T) ● 26°8'8"N, 81°47'13"W ±16ft ▲ 8ft



05 Apr 2022, 13:51:30

323 excavator removing material at station 3+50



☉ 142°SE (T) ☉ 26°8'14"N, 81°47'16"W ±13ft ▲ 12ft



05 Apr 2022, 15:05:19

326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 04/06/2022			
Inspectors: SB	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Wednesday	Contract Day: 171/365	Week: 25	Accident Report #: N/A
High Temp (°F): 88°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 3:56 PM +2.4'
Low Temp (°F): 76°F	Wind: 11 mph	Wind: 19 mph	Low Tide: 10:08 AM +1.3'
Canal Worked In: BB-BB / CC-CC	Stations Worked Between:	0+00 to 1+00 / 2+00 to 14+50	

General
<p>#1 – Prime Contractor – Quality Enterprises:</p> <ul style="list-style-type: none"> • Contractor has an excavator mounted on a barge staged in Canal BB-BB at station 0+50. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC at station 1+50. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102. • Contractor installed turbidity curtain across the mouth of Canal BB-BB. • Contractor used 323 excavator to check elevations and remove material between stations 0+00 and 0+50. • Contractor used push boat to transport barge, 323 excavator, and hopper back to Canal CC-CC. • Contractor used 326 excavator to redistribute removed material at the dewatering site at 1300 Curlew Avenue. • Contractor used 326 excavator to transfer removed material from the dewatering site to the dump truck. • 15 truckloads of material were taken off the site at 1300 Curlew Avenue by dump trucks. • Contractor installed turbidity curtain across the mouth of Canal CC-CC. • Contractor used 323 excavator to remove 1 hopper of material between stations 2+00 and 14+50. • Contractor used push boat to position barge as necessary for removing material. • Contractor used 326 excavator to transfer 1 hopper of material from hopper to dewatering site at 1300 Curlew Avenue.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	1	9	Mechanic	0	0
		Excavator Operator	2	9	Truck Driver	3	8	Assistant	1	9
		Technician	0	0	Superintendent	1	1	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	9
1	CAT 326	Excavator	1	1	7
1	02016	Front End Loader	1	0	0
1	FL6223TB	Push Boat	1	1	8
1	FL2474PP	Support Boat	1	0	0
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	1	1	8
1	MB28DQ	Dump truck	1	1	8
1	MB26DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 9:00 AM	To: 5:00 PM	8.0

SW 240 W 270 NW 300 330

☉ 286°W (T) ☉ 26°8'8"N, 81°47'16"W ±52ft ▲ 8ft



Push boat adjusting turbidity curtain across the mouth of Canal BB-BB

SE 150 S 180 SW 210 W 240 270

☀ 202°S (T) ☉ 26°8'14"N, 81°47'15"W ±45ft ▲ 9ft



06 Apr 2022 09:42:26

326 excavator transferring removed material from dewatering site at 1300 Curlew Avenue to dump truck

S 180 SW 210 240 W 270 300 N
☉ 243°SW (T) ☉ 26°8'15"N, 81°47'15"W ±13ft ▲ 8ft



326 excavator transferring removed material from dewatering site at 1300 Curlew Avenue to dump truck



☉ 234°SW (T) ☉ 26°8'13"N, 81°47'16"W ±26ft ▲ 8ft



323 excavator lifting spud to allow push boat to mobilize barge at the mouth of Canal CC-CC



☀ 262°W (T) ● 26°8'13"N, 81°47'0"W ±59ft ▲ 8ft



06 Apr 2022, 10:10:08

323 excavator removing checking depths and removing material from Station 14+50



323 excavator lifting spud to allow push boat to mobilize barge at station 13+00

SE S SW
120 150 80 210 240
☀ 178°S (T) ☉ 26°8'13"N, 81°47'16"W ±29ft ▲ 9ft



Turbidity curtain installed across the mouth of Canal CC-CC

NE 30 60 90 120 150 SE
☀ 89°E (T) ☉ 26°8'14"N, 81°47'16"W ±19ft ▲ 10ft



326 excavator transferring removed material from dewatering site at 1300 Curlew Avenue to dump truck

E SE S
60 90 120 150 180
☀ 127°SE (T) ☉ 26°8'13"N, 81°47'6"W ±39ft ▲ 8ft



06 Apr 2022, 14:59:59

323 excavator lifting spud to allow push boat to mobilize barge at station 7+00



☀ 83°E (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 11ft



06 Apr 2022, 15:24:49

326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue

E 90 SE 120 150 S 180
☀ 132°SE (T) ☉ 26°8'13"N, 81°47'16"W ±29ft ▲ 9ft



323 excavator lifting spud to allow push boat to mobilize barge and hopper at station 2+00



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 04/07/2022			
Inspectors: SB	Stantec PIN: 2028113191	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: Thursday	Contract Day: 172/365	Week: 25	Accident Report #: N/A
High Temp (°F): 87°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 4:30 PM +2.3'
Low Temp (°F): 76°F	Wind: 10 mph	Wind: 19 mph	Low Tide: 9:59 AM +1.4'
Canal Worked In: CC-CC	Stations Worked Between:	1+50 to 3+50	

General
<p>#1 – Prime Contractor – Quality Enterprises:</p> <ul style="list-style-type: none"> • Contractor has an excavator mounted on a barge staged in Canal CC-CC at station 1+50. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC at station 2+00. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102. • Contractor waited to let Police boat resident out of Canal CC-CC before attaching curtain or mobilizing barge. • Contractor installed turbidity curtain across the mouth of Canal CC-CC. • Contractor used 323 excavator to check elevations and remove material between stations 1+50 and 3+50. • Contractor used push boat to position barge as necessary for removing material as well as to open and close the turbidity curtain to let another resident exit Canal CC-CC. • Contractor used push boat to transport 323 excavator, barge, and hopper out to the bay to allow Morgan and Eklund survey boat access. • Contractor used push boat to transport 323 excavator, barge, and hopper back to Canal CC-CC station 1+50. • Contractor used front end loader to redistribute removed material at the dewatering site at 1300 Curlew Avenue. • Contractor used 326 excavator to transfer removed material from the dewatering site to the dump truck. • 8 truckloads of material were taken off the site at 1300 Curlew Avenue by dump trucks.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	1	9	Mechanic	0	0
		Excavator Operator	2	9	Truck Driver	2	8	Assistant	1	9
		Technician	0	0	Superintendent	1	1	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	7
1	CAT 323	Excavator	1	1	5
1	CAT 326	Excavator	1	1	7
1	02016	Front End Loader	1	1	1
1	FL6223TB	Push Boat	1	1	6
1	FL2474PP	Support Boat	1	1	1
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	1	1	8
1	MB28DQ	Dump truck	1	1	8
1	MB26DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:45 AM	To: 4:15 PM	7.5

S 180 SW 210 240 W 270 300

☉ 234°SW (T) ☉ 26°8'15"N, 81°47'15"W ±26ft ▲ 8ft



326 excavator transferring removed material from dewatering site to dump truck at 1300 Curlew Avenue




☀ 123°SE (T) ● 26°8'13"N, 81°47'16"W ±39ft ▲ 8ft



07 Apr 2022, 10:51:50

323 excavator lifting spud to allow push boat to mobilize barge at station 1+50



☀ 167°S (T) ● 26°8'13"N, 81°47'16"W ±19ft ▲ 8ft



07 Apr 2022, 10:52:01

Turbidity curtain installed across the mouth of Canal CC-CC

E 90 SE 120 150 S 180 210

☉ 151°SE (T) ☉ 26°8'13"N, 81°47'15"W ±13ft ▲ 8ft



07 Apr 2022, 11:08:06

323 excavator removing material from station 2+00 and transferring to hopper

E 90 SE 120 150 S 180 210
☀ 139°SE (T) ☉ 26°8'13"N, 81°47'15"W ±19ft ▲ 8ft



07 Apr 2022 11:08:35

323 excavator removing material from station 2+25 and transferring to hopper

E 90 SE 120 150 S 180

☀ 129°SE (T) ● 26°8'13"N, 81°47'16"W ±13ft ▲ 8ft



07 Apr 2022, 11:47:05


323 excavator lifting spud to allow push boat to mobilize barge at station 1+75

S 180 SW 240 W 270
50 | 180 | 210 | 240 | 270

☀ 220°SW (T) ● 26°8'13"N, 81°47'16"W ±16ft ▲ 8ft



Push boat opening turbidity curtain to allow resident to exit Canal CC-CC



☀ 51°NE (T) ☉ 26°8'14"N, 81°47'16"W ±49ft ▲ 9ft



07 Apr 2022, 13:46:06

326 excavator transferring removed material from dewatering site to dump truck at 1300 Curlew Avenue



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 04/08/2022			
Inspectors: SB	Stantec PIN: 2028113191	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: Friday	Contract Day: 173/365	Week: 25	Accident Report #: N/A
High Temp (°F): 78F	AM Conditions: Cloudy	PM Conditions: Cloudy	High Tide: 5:24 PM +2.1'
Low Temp (°F): 68°F	Wind: 9 mph	Wind: 14 mph	Low Tide: 10:08 AM +1.5'
Canal Worked In: N/A	Stations Worked Between:	N/A	

General
<p>#1 – Prime Contractor – Quality Enterprises:</p> <ul style="list-style-type: none"> • Contractor has an excavator mounted on a barge staged in Canal CC-CC at station 1+00. Contractor also has a push boat, a support boat, and two hoppers staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a long-reach excavator, a front end loader, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102. • Contractor pumped water out from the bottom of the barge. • Contractor greased 323 and 326 excavators and refilled with DEF. • Contractor filled water tank with fire hydrant outside of 1300 Curlew Avenue. • Contractor used water tank to clean all equipment on site and stationed in Canal CC-CC.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	1	6	Mechanic	0	0
		Excavator Operator	2	6	Truck Driver	0	0	Assistant	1	6
		Technician	0	0	Superintendent	1	2	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	2
1	CAT 323	Excavator	1	1	1
1	CAT 326	Excavator	1	1	1
1	02016	Front End Loader	1	0	0
1	FL6223TB	Push Boat	1	0	0
1	FL2474PP	Support Boat	1	0	0
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	1	2
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	0	0	0
1	MB28DQ	Dump truck	0	0	0
1	MB26DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 7:45 AM	To: 1:15 PM	6.0



☉ 236°SW (T) ☉ 26°8'13"N, 81°47'16"W ±19ft ▲ 9ft



Pumping water out of the bottom of the barge stated at station 1+00



☀ 148°SE (T) ● 26°8'13"N, 81°47'16"W ±13ft ▲ 6ft



2 empty hoppers staged at station 1+50



☀ 183°S (T) ☉ 26°8'15"N, 81°47'15"W ±32ft ▲ 8ft



08 Apr 2022 10:34:01

Removed material at the dewatering site at 1300 Curlew Avenue
