



WEEKLY SUMMARY REPORT – CONTRACT WEEK 35

21-036 EAST NAPLES BAY

DREDGING AND ROCK REMOVAL PROJECT



Date: 6/13/2022 to 6/17/2022			
Inspectors: Sam Boyd	Stantec PIN: 2028113191	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Days of Week: Monday to Friday	Contract Days: 239 to 243	Total Days: 365	Accident Report #: N/A
Canal(s) Worked In: X-X	Stations Worked Between: 7+00 to 13+75		

General

Remarks

#1 – Prime Contractor – Quality Enterprises:

Monday 06-13-2022:

- Contractor has a barge, an excavator, a support boat, 2 hoppers, and a push boat located in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor used push boat to transport barge and 323 excavator from Canal CC-CC to Canal X-X.
- Contractor used 326 excavator to redistribute removed material at 1300 Curlew Avenue.
- Contractor used support boat to install turbidity curtain across Canal X-X at station 11+00 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X.
- Contractor used 323 excavator to remove 4 hoppers of material between stations 12+00 and 13+75.
- Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X.
- Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue.

Tuesday 06-14-2022:

- Contractor has a barge and an excavator staged in Canal X-X at station 12+00. Contractor also has a support boat, 2 hoppers, and a push boat staged in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor used support boat to install turbidity curtain across Canal X-X at station 8+75 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X.
- Contractor used 323 excavator to remove 4 hoppers of material between stations 10+75 and 12+00.
- Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X.
- Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue.

Wednesday 06-15-2022:

- Contractor has a barge and an excavator staged in Canal X-X at station 10+50. Contractor also has a support boat, 2 hoppers, and a push boat staged in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300



WEEKLY SUMMARY REPORT – CONTRACT WEEK 35

21-036 EAST NAPLES BAY

DREDGING AND ROCK REMOVAL PROJECT



Curlew Avenue, Naples, FL, 34102.

- Seismic Survey crew came to site at 1300 Curlew Avenue.
- Contractor used push boat to transport survey crew to Canals W-W through M-M for pre-canal video survey.
- Contractor used support boat to install turbidity curtain across Canal X-X at station 8+75 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X and to let resident out of canal. Contractor moved curtain and attached it across Canal X-X at station 4+00.
- Contractor used 323 excavator to remove 4 hoppers of material between stations 9+50 and 10+75.
- Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X.
- Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue.

Thursday 06-16-2022:

- Contractor has a barge, an excavator, and a hopper staged in Canal X-X at station 10+50. Contractor also has a support boat, a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor used support boat to install turbidity curtain across Canal X-X at station 3+50 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X as well as to let resident out of the Canal.
- Contractor used 323 excavator to remove 4 hoppers of material between stations 7+50 and 9+75.
- Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X.
- Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue as well as to redistribute removed material.

Friday 06-17-2022:

- Contractor has a barge, an excavator, and a hopper staged in Canal X-X at station 10+50. Contractor also has a support boat, a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor used support boat to install turbidity curtain across Canal X-X at station 3+50 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X.
- Contractor used 323 excavator to remove 3 hoppers of material between stations 7+00 and 7+50.
- Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X.
- Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue as well as to redistribute removed material.



WEEKLY SUMMARY REPORT – CONTRACT WEEK 35
21-036 EAST NAPLES BAY
DREDGING AND ROCK REMOVAL PROJECT



- Contractor used push boat to transport barge, 323 excavator, and hopper from Canal X-X to Canal CC-CC.
- Contractor used small fuel cube to refuel 323 excavator.
- Contractor used water tank to clean equipment.
- Contractor took push boat over to city dock and left hoppers, barge, and 323 excavator in Canal CC-CC between stations 1+00 and 1+50.

Note: Daily reports with pictures attached for the week.



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 06/13/2022			
Inspectors: SB	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Monday	Contract Day: 239/365	Week: 35	Accident Report #: N/A
High Temp (°F): 90°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 11:58 AM +3.2'
Low Temp (°F): 76°F	Wind: 1 mph	Wind: 12 mph	Low Tide: 6:39 AM +1.2'
Canal Worked In: X-X	Stations Worked Between:	12+00 to 13+75	

General

#1 – Prime Contractor – Quality Enterprises:


- Contractor has a barge, an excavator, a support boat, 2 hoppers, and a push boat located in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor used push boat to transport barge and 323 excavator from Canal CC-CC to Canal X-X.
- Contractor used 326 excavator to redistribute removed material at 1300 Curlew Avenue.
- Contractor used support boat to install turbidity curtain across Canal X-X at station 11+00 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X.
- Contractor used 323 excavator to remove 4 hoppers of material between stations 12+00 and 13+75.
- Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X.
- Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	1	9	Mechanic	0	0
		Excavator Operator	2	9	Truck Driver	0	0	Assistant	1	9
		Technician	0	0	Superintendent	0	0	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	9
1	CAT 326	Excavator	1	1	6
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	1	7
1	FL2474PP	Support Boat	1	1	2
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	0	0	0
1	MB3DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:45 AM	To: 4:45 PM	8.0



326 excavator redistributing removed material at dewatering site at 1300 Curlew Avenue


SW W NW
210 240 270 300 330

☉ 279°W (T) ☉ 26°8'5"N, 81°47'0"W ±13ft ▲ 9ft



13 Jun 2022, 09:01:37

323 excavator removing material from station 13+50




☀ 293°W (T) ● 26°8'4"N, 81°47'4"W ±13ft ▲ 7ft



13 Jun 2022, 09:45:17

Support boat being used to open turbidity curtain to allow push boat to transport full hopper back to Canal CC-CC

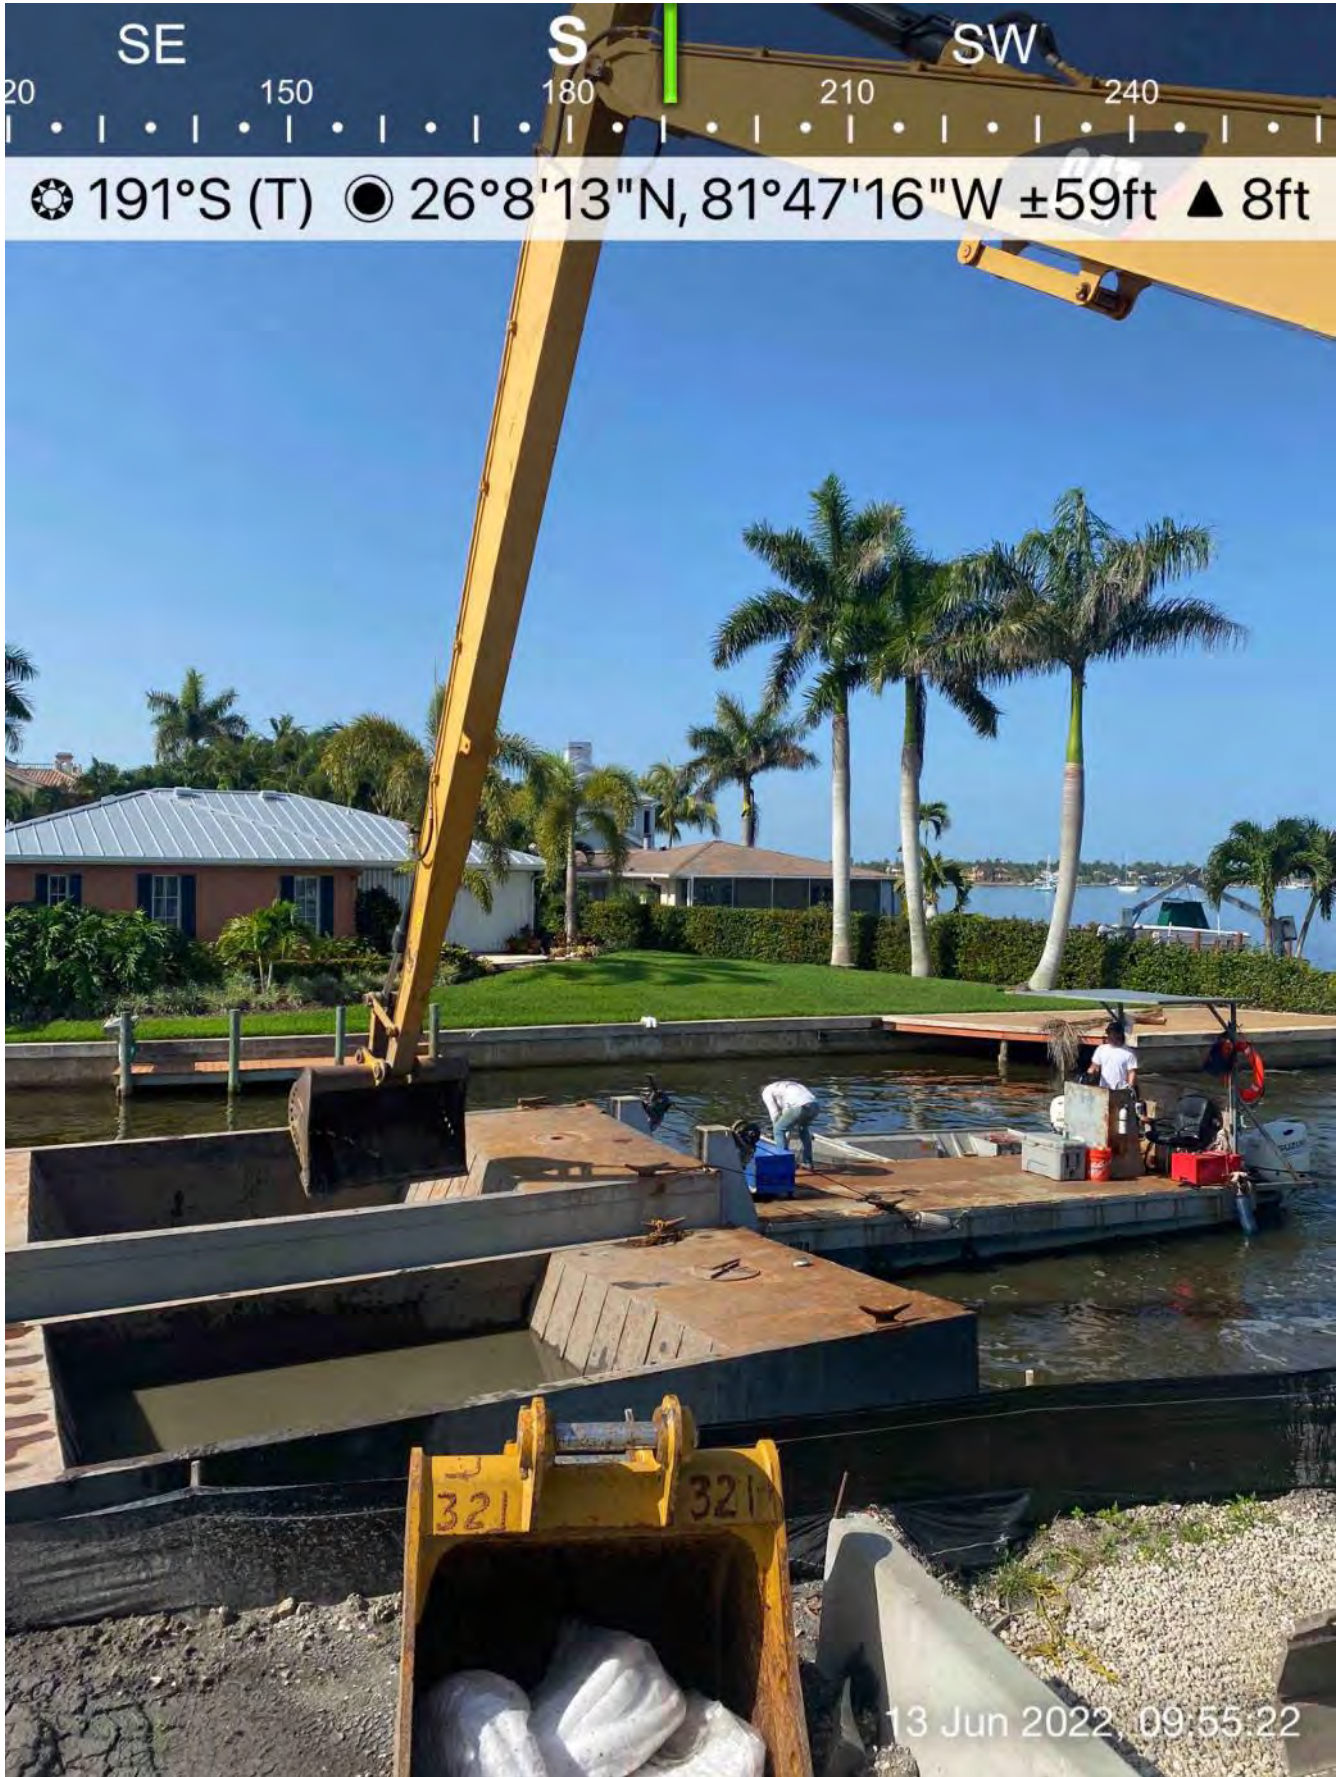

Push boat dropping off full hopper of material in Canal CC-CC



☉ 169°S (T) ● 26°8'14"N, 81°47'16"W ±13ft ▲ 10ft



13 Jun 2022, 11:19:29

326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue



☀ 16°N (T) ● 26°8'4"N, 81°47'3"W ±16ft ▲ 11ft



323 excavator lifting spud to allow push boat to mobilize barge at station 12+00



323 excavator transferring removed material to hopper at station 11+75



☉ 58°NE (T) ☉ 26°8'4"N, 81°47'4"W ±16ft ▲ 7ft



323 excavator transferring removed material to hopper at station 11+50



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 06/14/2022			
Inspectors: SB	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Tuesday	Contract Day: 240/365	Week: 35	Accident Report #: N/A
High Temp (°F): 91°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 12:38 PM +3.3'
Low Temp (°F): 78°F	Wind: 6 mph	Wind: 10 mph	Low Tide: 7:24 AM +1.3'
Canal Worked In: X-X	Stations Worked Between:	10+75 to 12+00	

General
<p>#1 – Prime Contractor – Quality Enterprises:</p> <ul style="list-style-type: none"> • Contractor has a barge and an excavator staged in Canal X-X at station 12+00. Contractor also has a support boat, 2 hoppers, and a push boat staged in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102. • Contractor used support boat to install turbidity curtain across Canal X-X at station 8+75 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X. • Contractor used 323 excavator to remove 4 hoppers of material between stations 10+75 and 12+00. • Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X. • Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	1	9	Mechanic	0	0
		Excavator Operator	1	9	Truck Driver	0	0	Assistant	1	9
		Technician	0	0	Superintendent	0	0	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	9
1	CAT 326	Excavator	1	1	4
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	1	9
1	FL2474PP	Support Boat	1	1	2
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	0	0	0
1	MB3DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 9:00 AM	To: 5:00 PM	8.0

S SW W
180 210 240 270
50
☀ 220°SW (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 10ft



Push boat dropping off full hopper of material in Canal CC-CC



☀ 291°W (T) ☉ 26°8'4"N, 81°47'5"W ±42ft ▲ 8ft



14 Jun 2022, 09:45:47

Turbidity curtain installed across Canal X-X at station 8+75



☀ 16°N (T) ☉ 26°8'4"N, 81°47'4"W ±13ft ▲ 12ft



14 Jun 2022, 09:46:33

323 excavator removing material from station 11+50

S 180 210 SW 240 W 270
☀ 222°SW (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 10ft



Push boat transporting empty hopper from Canal CC-CC to Canal X-X



☀ 310°NW (T) ● 26°8'4"N, 81°47'4"W ±42ft ▲ 8ft



323 excavator transferring removed material to hopper at station 11+00



14 Jun 2022, 14:41:51

Support boat opening turbidity curtain to allow push boat to transport full hopper from Canal X-X to Canal CC-CC

SE S SW
120 150 180 210 240

☉ 172°S (T) ● 26°8'14"N, 81°47'16"W ±13ft ▲ 9ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue



☀ 303°NW (T) ● 26°8'4"N, 81°47'4"W ±16ft ▲ 8ft



14 Jun 2022, 16:28:51

323 excavator lifting spud to allow push boat to mobilize barge at station 12+00



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 06/15/2022			
Inspectors: SB	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Wednesday	Contract Day: 241/365	Week: 35	Accident Report #: N/A
High Temp (°F): 92°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 1:21 PM +3.4'
Low Temp (°F): 76°F	Wind: 4 mph	Wind: 9 mph	Low Tide: 8:11 AM +1.4'
Canal Worked In: X-X	Stations Worked Between:	9+50 to 10+75	

General
<p>#1 – Prime Contractor – Quality Enterprises:</p> <ul style="list-style-type: none"> • Contractor has a barge and an excavator staged in Canal X-X at station 10+50. Contractor also has a support boat, 2 hoppers, and a push boat staged in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102. • Seismic Survey crew came to site at 1300 Curlew Avenue. • Contractor used push boat to transport survey crew to Canals W-W through M-M for pre-canal video survey. • Contractor used support boat to install turbidity curtain across Canal X-X at station 8+75 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X and to let resident out of canal. Contactor moved curtain and attached it across Canal X-X at station 4+00. • Contractor used 323 excavator to remove 4 hoppers of material between stations 9+50 and 10+75. • Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X. • Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	1	9	Mechanic	0	0
		Excavator Operator	2	9	Truck Driver	0	0	Assistant	1	9
		Technician	0	0	Superintendent	0	0	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	7
1	CAT 323	Excavator	1	1	7
1	CAT 326	Excavator	1	1	3
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	1	9
1	FL2474PP	Support Boat	1	1	3
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	0	0	0
1	MB3DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:
	Seismic Survey Crew	8:00 am	9:30 am

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:30 AM	To: 4:30 PM	8.0



☀ 312°NW (T) ● 26°8'4"N, 81°47'4"W ±22ft ▲ 8ft



323 excavator on barge at station 10+50

W 240 W 270 00 NW 330 N 0
☉ 298°NW (T) ☉ 26°8'5"N, 81°47'5"W ±114ft ▲ 10ft



323 excavator lifting spud to allow push boat to mobilize barge at station 12+00



☀ 357°N (T) ☉ 26°8'4"N, 81°47'5"W ±13ft ▲ 12ft



15 Jun 2022, 09:56:30

323 excavator removing material from station 10+75 and transferring to hopper



☉ 289°W (T) ● 26°8'4"N, 81°47'5"W ±22ft ▲ 8ft



Turbidity curtain installed across Canal X-X at station 8+75



☀ 298°NW (T) ● 26°8'4"N, 81°47'5"W ±13ft ▲ 8ft



15 Jun 2022, 10:47:04

Support boat opening turbidity curtain to allow resident to exit Canal X-X



☉ 233°SW (T) ☉ 26°8'14"N, 81°47'15"W ±39ft ▲ 8ft



Push boat dropping off full hopper of material in Canal CC-CC at station 1+50



☀ 70°E (T) ● 26°8'13"N, 81°47'16"W ±26ft ▲ 8ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue

NW

N

NE

330

0

30

60

☀ 17°N (T) ☉ 26°8'4"N, 81°47'5"W ±13ft ▲ 8ft



15 Jun 2022, 14:30:05

323 excavator removing material from station 10+00

W 270 NW 330 N 0
40 300 0
☀ 311°NW (T) ● 26°8'4"N, 81°47'9"W ±29ft ▲ 8ft



15 Jun 2022, 14:59:49

Support boat opening turbidity curtain to allow push boat to transport full hopper from Canal X-X to Canal CC-CC



☀ 310°NW (T) ● 26°8'4"N, 81°47'5"W ±13ft ▲ 7ft



15 Jun 2022, 15:57:30

323 excavator removing material from station 9+75



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 06/16/2022			
Inspectors: SB	Stantec PIN: 2028113191	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: Thursday	Contract Day: 242/365	Week: 35	Accident Report #: N/A
High Temp (°F): 93°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 2:11 PM +3.3'
Low Temp (°F): 76°F	Wind: 5 mph	Wind: 9 mph	Low Tide: 9:02 AM +1.4'
Canal Worked In: X-X	Stations Worked Between:	7+50 to 9+50	


General
<p>#1 – Prime Contractor – Quality Enterprises:</p> <ul style="list-style-type: none"> • Contractor has a barge, an excavator, and a hopper staged in Canal X-X at station 10+50. Contractor also has a support boat, a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102. • Contractor used support boat to install turbidity curtain across Canal X-X at station 3+50 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X as well as to let resident out of the Canal. • Contractor used 323 excavator to remove 4 hoppers of material between stations 7+50 and 9+75. • Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X. • Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue as well as to redistribute removed material.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	1	0.5	Boat Captain	1	9	Mechanic	0	0
		Excavator Operator	2	9	Truck Driver	0	0	Assistant	1	9
		Technician	0	0	Superintendent	1	0.5	VP	0	0


Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator	1	1	9
1	CAT 326	Excavator	1	1	4
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	1	9
1	FL2474PP	Support Boat	1	1	4
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	0	0	0
1	MB3DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:


Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 9:00 AM	To: 5:00 PM	8.0

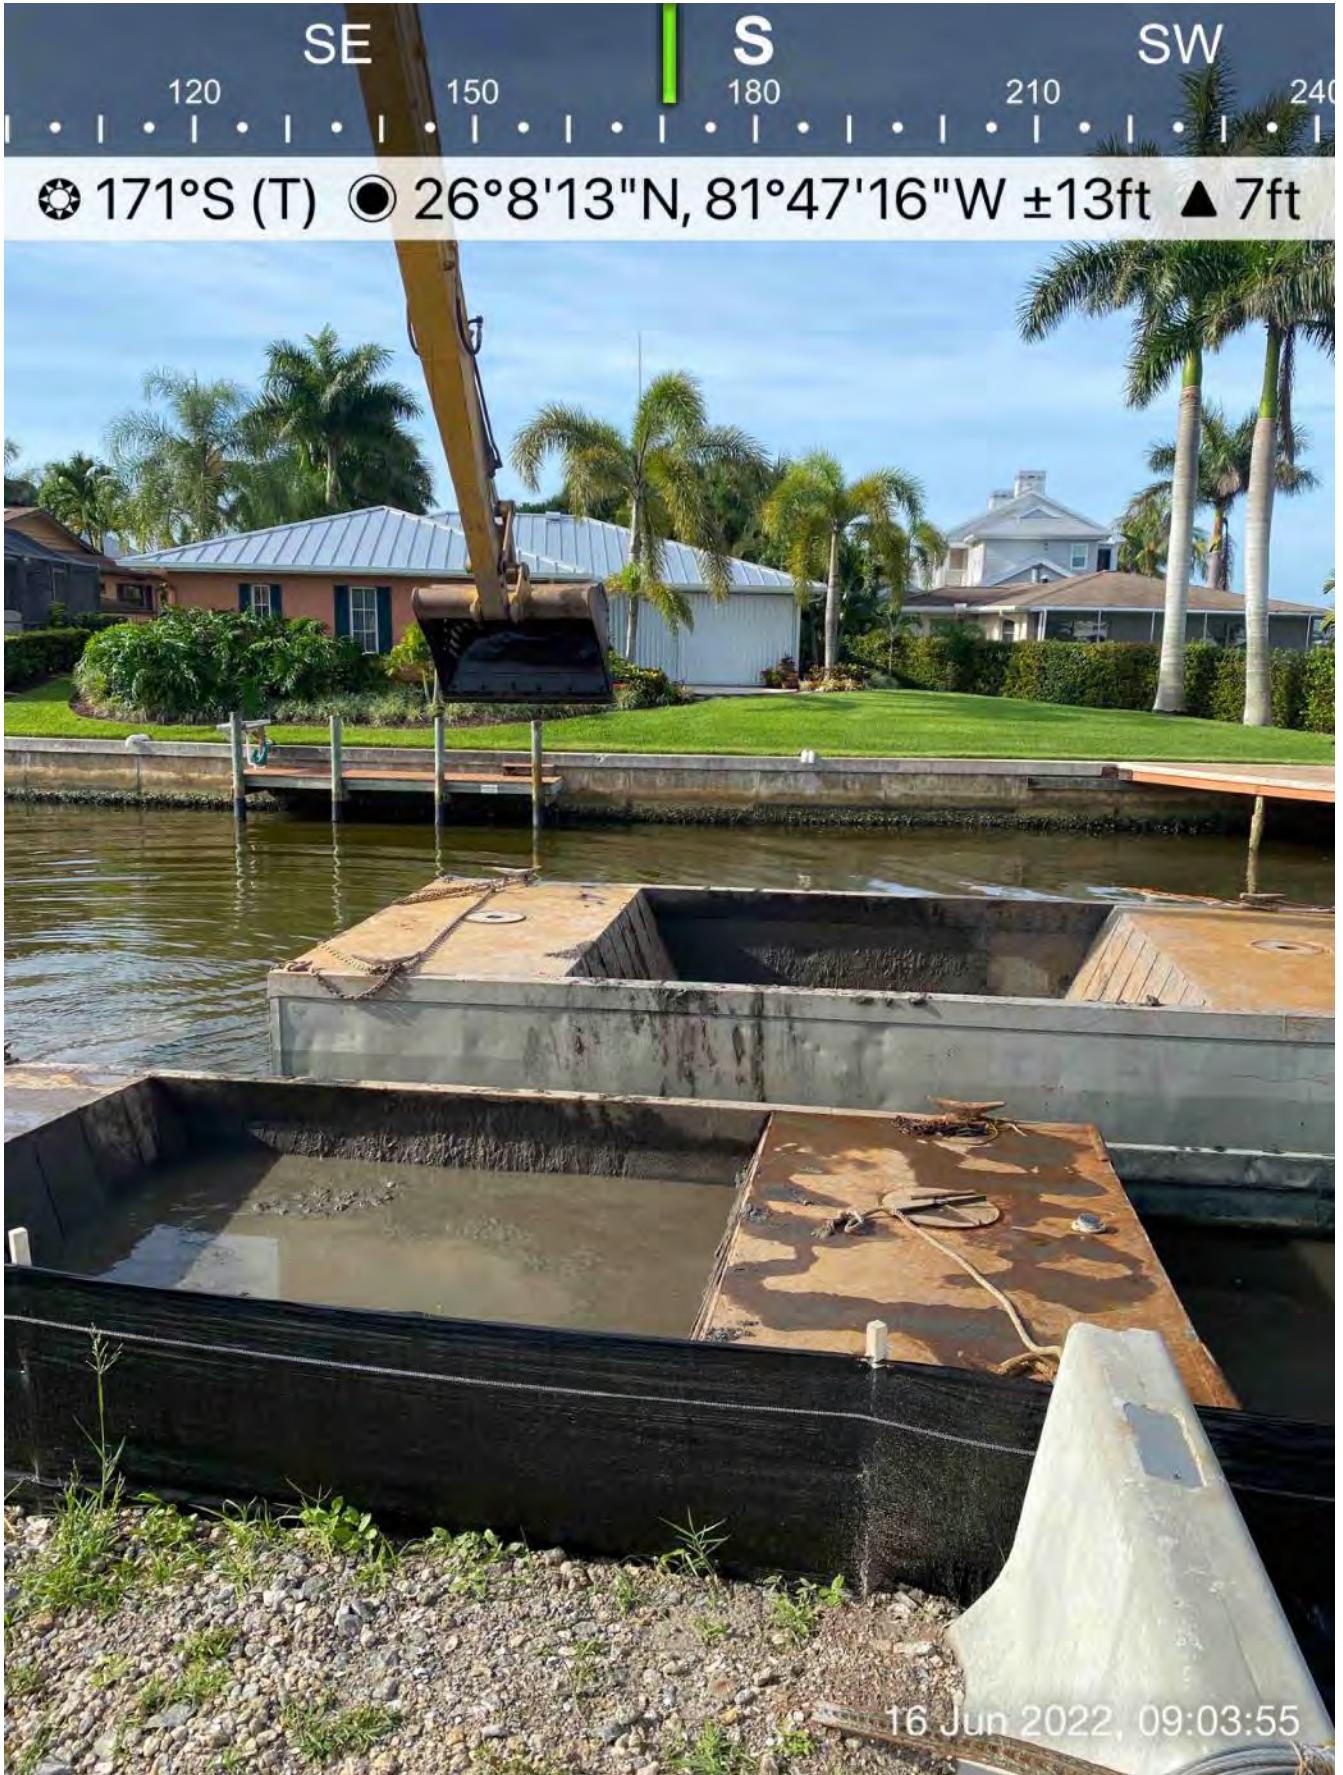

Full hopper of material and empty hopper in Canal CC-CC at station 1+50



Push boat transporting empty hopper from Canal CC-CC to Canal X-X



☀ 298°NW (T) ● 26°8'4"N, 81°47'11"W ±13ft ▲ 8ft



16 Jun 2022, 09:16:54

Turbidity curtain installed across Canal X-X at station 3+50



☀ 10°N (T) ● 26°8'4"N, 81°47'6"W ±13ft ▲ 9ft



16 Jun 2022, 09:22:46

323 excavator removing material from station 9+25

E SE S
60 90 120 150 180
☀ 122°SE (T) ● 26°8'13"N, 81°47'16"W ±13ft ▲ 9ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue



☀ 130°SE (T) ● 26°8'14"N, 81°47'16"W ±13ft ▲ 12ft



16 Jun 2022, 13:37:31

326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue

S 180 SW 210 240 W 270
☀ 227°SW (T) ● 26°8'13"N, 81°47'16"W ±32ft ▲ 8ft



Push boat dropping off a full hopper of removed material in Canal CC-CC



☀ 10°N (T) ● 26°8'4"N, 81°47'8"W ±16ft ▲ 9ft



323 excavator lifting spud to allow push boat to mobilize barge at station 7+75



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 06/17/2022			
Inspectors: SB	Stantec PIN: 2028113191	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: Friday	Contract Day: 243/365	Week: 35	Accident Report #: N/A
High Temp (°F): 94°F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 3:14 PM +3.1'
Low Temp (°F): 78°F	Wind: 7 mph	Wind: 9 mph	Low Tide: 9:56 AM +1.4'
Canal Worked In: X-X	Stations Worked Between:	7+00 to 7+50	

General
<p>#1 – Prime Contractor – Quality Enterprises:</p> <ul style="list-style-type: none"> • Contractor has a barge, an excavator, and a hopper staged in Canal X-X at station 10+50. Contractor also has a support boat, a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 1+50. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102. • Contractor used support boat to install turbidity curtain across Canal X-X at station 3+50 as well as to remove and reattach curtain as necessary for push boat to transport hoppers to and from canal X-X. • Contractor used 323 excavator to remove 3 hoppers of material between stations 7+00 and 7+50. • Contractor used push boat to position barge as necessary for removing material as well as for transporting full hoppers back to Canal CC-CC and empty hoppers back to Canal X-X. • Contractor used 326 excavator to transfer removed material from hoppers to dewatering site at 1300 Curlew Avenue as well as to redistribute removed material. • Contractor used push boat to transport barge, 323 excavator, and hopper from Canal X-X to Canal CC-CC. • Contractor used small fuel cube to refuel 323 excavator. • Contractor used water tank to clean equipment. • Contractor took push boat over to city dock and left hoppers, barge, and 323 excavator in Canal CC-CC between stations 1+00 and 1+50.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Boat Captain	1	9	Mechanic	0	0
		Excavator Operator	2	9	Truck Driver	0	0	Assistant	1	9
		Technician	0	0	Superintendent	0	0	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	5
1	CAT 323	Excavator	1	1	5
1	CAT 326	Excavator	1	1	3
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	1	6
1	FL2474PP	Support Boat	1	1	2
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	1	1
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Dump truck	0	0	0
1	MB3DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	DRHS18	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:30 AM	To: 4:30 PM	8.0

SE S SW
120 150 180 210 240

☀ 186°S (T) ☉ 26°8'15"N, 81°47'15"W ±19ft ▲ 10ft



Removed material at dewatering site at 1300 Curlew Avenue



Support boat opening turbidity curtain to allow push boat to transport full hopper from Canal X-X to Canal CC-CC

SE S SW
120 150 180 210 240

☉ 171°S (T) ☉ 26°8'14"N, 81°47'16"W ±13ft ▲ 9ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue

SE 150 S 180 210 SW 240 W 270

☀ 201°S (T) ☉ 26°8'4"N, 81°47'8"W ±22ft ▲ 8ft



17 Jun 2022, 09:56:05

323 excavator removing material from station 7+50 and transferring it to hopper



☀ 37°NE (T) ● 26°8'4"N, 81°47'8"W ±55ft ▲ 9ft



323 excavator lifting spud to allow push boat to mobilize barge at station 7+00

S 180 SW 210 240 W 270 300
☀ 231°SW (T) ☉ 26°8'13"N, 81°47'16"W ±19ft ▲ 8ft



Push boat transporting barge and 323 excavator back to Canal CC-CC

SE S SW
120 150 180 210
☉ 163°S (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 12ft



Small fuel cube being used to refuel 323 excavator on barge at station 1+25 in Canal CC-CC
