



# WEEKLY SUMMARY REPORT – CONTRACT WEEK 39

21-036 EAST NAPLES BAY

## DREDGING AND ROCK REMOVAL PROJECT



Date: <b>7/11/2022 to 7/15/2022</b>			
Inspectors: <b>Sam Boyd</b>	Stantec PIN: <b>2028113191</b>	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Days of Week: <b>Monday to Friday</b>	Contract Days: <b>267 to 271</b>	Total Days: <b>365</b>	Accident Report #: <b>N/A</b>
Canal(s) Worked In: <b>X-X</b>	Stations Worked Between: <b>0+00 to 0+75</b>		

### General

### Remarks

#### **#1 – Prime Contractor – Quality Enterprises:**

##### Monday 07-11-2022:

- Contractor has a barge, an excavator, 2 hoppers, a push boat, and a support boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Fuel truck came to site at 1300 Curlew Avenue and refilled large and small fuel cube.
- Mechanic came to site at 1300 Curlew Avenue to inspect error codes on 323 excavator.
- Contractor used push boat to transport barge and 323 excavator from Canal CC-CC to Canal X-X.
- Contractor used support boat to install turbidity curtain across the mouth of Canal X-X.
- Contractor used 323 excavator to grind rock between stations 0+00 and 0+50.
- Contractor used push boat to position barge as necessary for grinding rock.
- Contractor pumped water out from bottom of barge.
- 2 Small dump trucks came to site at 1300 Curlew Avenue
- Contractor used 326 excavator to transfer removed material from dewatering site to dump truck beds at 1300 Curlew Avenue as well as to redistribute removed material at dewatering site.
- Dump trucks took removed material off site.
- Contractor switched from Epiroc grinder to bucket and removed 1 hopper of material from station 0+25.

##### Tuesday 07-12-2022:

- Contractor has a barge, an excavator, and a hopper stationed outside the mouth of Canal X-X. Contractor also has a hopper, a push boat, and a support boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Push boat was sinking at station 2+00 in Canal CC-CC.
- Contractor used 326 excavator to lift push boat out of the water.
- Contractor used water pump to pump water out from bottom of push boat hull.
- Two mechanics came to site to inspect the boat motors.
- Contractor used 326 excavator to redistribute removed material at dewatering site as well as to move Jersey



## WEEKLY SUMMARY REPORT – CONTRACT WEEK 39

21-036 EAST NAPLES BAY

### DREDGING AND ROCK REMOVAL PROJECT



barriers, and to transport support boat from Canal CC-CC to the lot at 1300 Curlew Avenue.

- Crane truck came to site at 1300 Curlew Avenue.
- Contractor attempted to lift push boat onto the lot with crane and 326 excavator.
- Contractor used water tank to clean push boat.

#### Wednesday 07-13-2022:

- Contractor has a barge, an excavator, and a hopper stationed outside the mouth of Canal X-X. Contractor also has a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a support boat, a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Dump truck came to site at 1300 Curlew Avenue.
- Contractor used 326 excavator to redistribute removed material at dewatering site as well as to transfer removed material from dewatering site to dump truck bed.
- Dump truck took removed material off site.
- Contractor put door tags on Canal W-W residents' doors and boats.
- Contractor took push boat from Canal CC-CC to Canal X-X. Contractor pumped water out from the bottom of the barge. Contractor took push boat over to city dock.

#### Thursday 07-14-2022:

- Contractor has a barge, an excavator, and a hopper stationed outside the mouth of Canal X-X. Contractor also has a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a support boat, a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor transported support boat to Jersey barriers on site at 1300 Curlew Avenue.
- Dump truck came to site at 1300 Curlew Avenue.
- Contractor used 326 excavator to redistribute removed material at dewatering site as well as to transfer removed material from dewatering site to dump truck bed.
- Dump truck took removed material off site.
- Mechanic came to site at 1300 Curlew Avenue to inspect support boat motor.
- Contractor installed turbidity curtain across the mouth of Canal X-X.
- Contractor used 323 excavator to remove 2 hoppers of material between stations 0+25 and 0+75.
- Contractor used push boat to position barge as necessary for removing material as well as to transport full hoppers of material to Canal CC-CC and empty hoppers of material to Canal X-X
- Contractor used 326 excavator to transfer 2 hoppers of material from hopper to dewatering site at 1300 Curlew Avenue.



## WEEKLY SUMMARY REPORT – CONTRACT WEEK 39

21-036 EAST NAPLES BAY

### DREDGING AND ROCK REMOVAL PROJECT



#### Friday 07-15-2022:

- Contractor has a barge, an excavator, and a hopper stationed outside the mouth of Canal X-X. Contractor also has a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a support boat, a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor installed turbidity curtain across the mouth of Canal X-X.
- Contractor used 323 excavator to remove 2 hoppers of material between stations 0+00 and 0+75.
- Contractor used push boat to position barge as necessary for removing material as well as to transport full hoppers of material to Canal CC-CC and empty hoppers of material to Canal X-X.
- Contractor used 326 excavator to transfer 2 hoppers of material from hopper to dewatering site at 1300 Curlew Avenue as well as to redistribute removed material at the dewatering site.
- Trash truck came to site at 1300 Curlew Avenue to remove trash from site.
- Contractor used push boat to transport hopper, 323 excavator, and barge back to Canal CC-CC.
- Contractor pumped water out of hoppers.
- Contractor took boat over to city dock.

**Note: Daily reports with pictures attached for the week.**



**DAILY REPORT OF CONSTRUCTION**  
 21-036 EAST NAPLES BAY  
 DREDGING AND ROCK REMOVAL PROJECT



Date: <b>07/11/2022</b>			
Inspectors: <b>SB</b>	Stantec PIN: <b>2028113191</b>	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: <b>Monday</b>	Contract Day: <b>267/365</b>	Week: <b>39</b>	Accident Report #: <b>N/A</b>
High Temp (°F): <b>89°F</b>	AM Conditions: <b>Sunny</b>	PM Conditions: <b>Sunny</b>	High Tide: <b>10:54 AM +3.1'</b>
Low Temp (°F): <b>79°F</b>	Wind: <b>6 mph</b>	Wind: <b>10 mph</b>	Low Tide: <b>6:35 PM -0.6'</b>
Canal Worked In: <b>X-X</b>	Stations Worked Between:	<b>0+00 to 0+50</b>	

<b>General</b>
<p><b>#1 – Prime Contractor – Quality Enterprises:</b></p> <ul style="list-style-type: none"> <li>• Contractor has a barge, an excavator, 2 hoppers, a push boat, and a support boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.</li> <li>• Fuel truck came to site at 1300 Curlew Avenue and refilled large and small fuel cube.</li> <li>• Mechanic came to site at 1300 Curlew Avenue to inspect error codes on 323 excavator.</li> <li>• Contractor used push boat to transport barge and 323 excavator from Canal CC-CC to Canal X-X.</li> <li>• Contractor used support boat to install turbidity curtain across the mouth of Canal X-X.</li> <li>• Contractor used 323 excavator to grind rock between stations 0+00 and 0+50.</li> <li>• Contractor used push boat to position barge as necessary for grinding rock.</li> <li>• Contractor pumped water out from bottom of barge.</li> <li>• 2 Small dump trucks came to site at 1300 Curlew Avenue</li> <li>• Contractor used 326 excavator to transfer removed material from dewatering site to dump truck beds at 1300 Curlew Avenue as well as to redistribute removed material at dewatering site.</li> <li>• Dump trucks took removed material off site.</li> <li>• Contractor switched from Epiroc grinder to bucket and removed 1 hopper of material from station 0+25.</li> </ul>

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: <b>Quality Enterprises</b>	PM	0	0	Boat Captain	1	9	Mechanic	1	2
		Excavator Operator	2	9	Truck Driver	2	9	Assistant	1	9
		Technician	0	0	Superintendent	0	0	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	8
1	CAT 323	Excavator	1	1	7
1	CAT 326	Excavator	1	1	4
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	1	7
1	FL2474PP	Support Boat	1	1	3
1	N3758Z	Fuel Truck	1	1	1
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	1	1	9
1	PB727E	Small Dump truck	1	1	9
1	MB27DQ	Dump truck	0	0	0
1	MB8DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	MB26DQ	Utility Truck	1	1	2
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0


Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:30 AM	To: 4:30 PM	8.0

SE S SW  
120 150 180 210 240  
186°S (T) 26°8'14"N, 81°47'16"W ±22ft ▲ 9ft



Fuel truck on site at 1300 Curlew Avenue refilling small and large fuel cubes



☀ 210°SW (T) ● 26°8'14"N, 81°47'15"W ±13ft ▲ 9ft



326 excavator transferring removed material from dewatering site to dump truck bed at 1300 Curlew Avenue

S 30 SW 210 240 W 270 NW 300  
☉ 251°W (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 9ft



323 excavator lifting spud to allow push boat to transport barge from Canal CC-CC to Canal X-X



W NW N  
240 270 300 330 0  
304°NW (T) 26°8'4"N, 81°47'15"W ±13ft ▲ 10ft




323 excavator grinding rock at station 0+00

SW 240 W 270 NW 330 N 0  
294°NW (T) 26°8'4"N, 81°47'15"W ±26ft ▲ 8ft



323 excavator grinding rock at station 0+25



Contractor pumping water out of the bottom of the barge at station 0+00

W 270 NW 330 N 0  
40 270 300 330 0

☀ 310°NW (T) ☉ 26°8'5"N, 81°47'15"W ±32ft ▲ 9ft



323 excavator grinding rock at station 0+50

SE 150 S 180 SW 210 240  
☀ 196°S (T) ☉ 26°8'15"N, 81°47'15"W ±13ft ▲ 8ft



Removed material at dewatering site at 1300 Curlew Avenue

E 90 SE 120 150 S 180 2  
☀ 138°SE (T) ● 26°8'14"N, 81°47'16"W ±52ft ▲ 8ft



326 excavator transferring removed material from dewatering site to dump truck bed at 1300 Curlew Avenue



11 Jul 2022, 16:13:37

Push boat transporting hopper from Canal X-X to Canal CC-CC

SW 240 W 270 NW 330 N 0  
294°NW (T) 26°8'4"N, 81°47'15"W ±36ft ▲ 10ft



323 excavator removing material from station 0+25 and transferring to hopper





**DAILY REPORT OF CONSTRUCTION**  
 21-036 EAST NAPLES BAY  
 DREDGING AND ROCK REMOVAL PROJECT



Date: <b>07/12/2022</b>			
Inspectors: <b>SB</b>	Stantec PIN: <b>2028113191</b>	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: <b>Tuesday</b>	Contract Day: <b>268/365</b>	Week: <b>39</b>	Accident Report #: <b>N/A</b>
High Temp (°F): <b>89°F</b>	AM Conditions: <b>Sunny</b>	PM Conditions: <b>Sunny</b>	High Tide: <b>11:47 AM +3.3'</b>
Low Temp (°F): <b>78°F</b>	Wind: <b>5 mph</b>	Wind: <b>8 mph</b>	Low Tide: <b>7:27 PM -0.8'</b>
Canal Worked In: <b>N/A</b>	Stations Worked Between:	<b>N/A</b>	


<b>General</b>
<p><b>#1 – Prime Contractor – Quality Enterprises:</b></p> <ul style="list-style-type: none"> <li>• Contractor has a barge, an excavator, and a hopper stationed outside the mouth of Canal X-X. Contractor also has a hopper, a push boat, and a support boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.</li> <li>• Push boat was sinking at station 2+00 in Canal CC-CC.</li> <li>• Contractor used 326 excavator to lift push boat out of the water.</li> <li>• Contractor used water pump to pump water out from bottom of push boat hull.</li> <li>• Two mechanics came to site to inspect the boat motors.</li> <li>• Contractor used 326 excavator to redistribute removed material at dewatering site as well as to move Jersey barriers, and to transport support boat from Canal CC-CC to the lot at 1300 Curlew Avenue.</li> <li>• Crane truck came to site at 1300 Curlew Avenue.</li> <li>• Contractor attempted to lift push boat onto the lot with crane and 326 excavator.</li> <li>• Contractor used water tank to clean push boat.</li> </ul>

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: <b>Quality Enterprises</b>	PM	0	0	Boat Captain	1	9	Mechanic	2	4
		Excavator Operator	2	9	Truck Driver	1	4	Assistant	1	9
		Technician	0	0	Superintendent	1	0.5	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	0
1	CAT 323	Excavator	1	1	0
1	CAT 326	Excavator	1	1	8
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	0	0
1	FL2474PP	Support Boat	1	0	0
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	1	1
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Small Dump truck	0	0	0
1	MB27DQ	Dump truck	0	0	0
1	MB8DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	MB26DQ	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0
1	N8105X	Crane Truck	1	1	3

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:30 AM	To: 4:30 PM	8.0

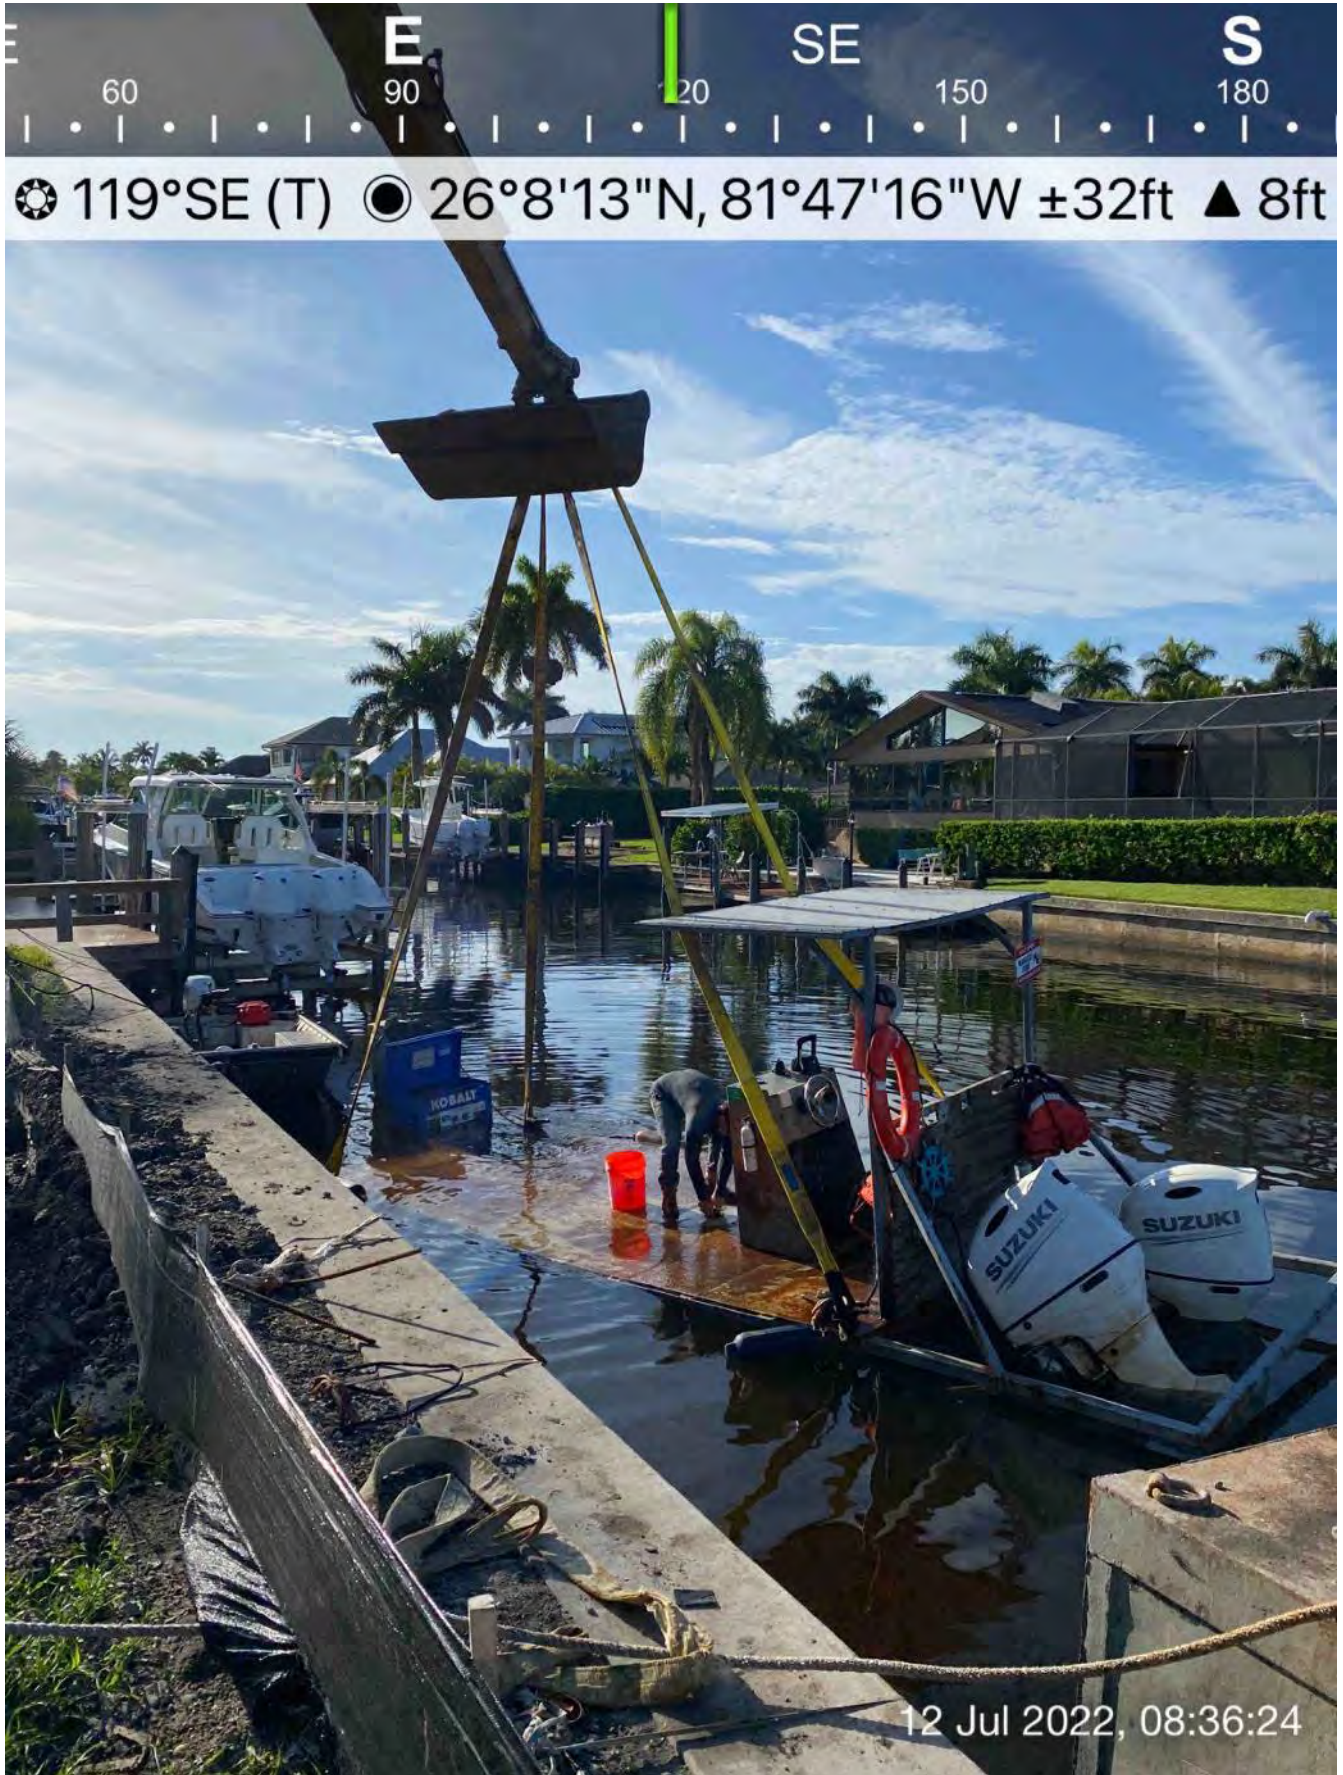

326 excavator lifting push boat and contractor opening manhole to pump water out from hull of push boat

NE 60 E 90 SE 150 S 180

☀ 112°E (T) ☉ 26°8'13"N, 81°47'16"W ±42ft ▲ 8ft



12 Jul 2022, 10:02:15

Contractor and Mechanic inspecting the push boat motors



☀ 175°S (T) ☉ 26°8'14"N, 81°47'16"W ±36ft ▲ 9ft



326 excavator, crane truck, and support boat on site at 1300 Curlew Avenue



**DAILY REPORT OF CONSTRUCTION**  
 21-036 EAST NAPLES BAY  
 DREDGING AND ROCK REMOVAL PROJECT



Date: <b>07/13/2022</b>			
Inspectors: <b>SB</b>	Stantec PIN: <b>2028113191</b>	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: <b>Wednesday</b>	Contract Day: <b>269/365</b>	Week: <b>39</b>	Accident Report #: <b>N/A</b>
High Temp (°F): <b>93°F</b>	AM Conditions: <b>Sunny</b>	PM Conditions: <b>Sunny</b>	High Tide: <b>12:36 PM +3.4'</b>
Low Temp (°F): <b>78°F</b>	Wind: <b>5 mph</b>	Wind: <b>11 mph</b>	Low Tide: <b>8:17 PM -0.8'</b>
Canal Worked In: <b>N/A</b>	Stations Worked Between:	<b>N/A</b>	

<b>General</b>
<p><b>#1 – Prime Contractor – Quality Enterprises:</b></p> <ul style="list-style-type: none"> <li>• Contractor has a barge, an excavator, and a hopper stationed outside the mouth of Canal X-X. Contractor also has a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a support boat, a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.</li> <li>• Dump truck came to site at 1300 Curlew Avenue.</li> <li>• Contractor used 326 excavator to redistribute removed material at dewatering site as well as to transfer removed material from dewatering site to dump truck bed.</li> <li>• Dump truck took removed material off site.</li> <li>• Contractor put door tags on Canal W-W residents' doors and boats.</li> <li>• Contractor took push boat from Canal CC-CC to Canal X-X. Contractor pumped water out from the bottom of the barge. Contractor took push boat over to city dock.</li> </ul>

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: <b>Quality Enterprises</b>	PM	0	0	Boat Captain	1	9	Mechanic	0	0
		Excavator Operator	2	9	Truck Driver	1	9	Assistant	1	9
		Technician	0	0	Superintendent	0	0	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	1
1	CAT 323	Excavator	1	1	1
1	CAT 326	Excavator	1	1	4
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	1	3
1	FL2474PP	Support Boat	1	0	0
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	1	1	9
1	PB727E	Small Dump truck	0	0	0
1	MB27DQ	Dump truck	0	0	0
1	MB8DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	MB26DQ	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0
1	N8105X	Crane Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:


Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:30 AM	To: 4:30 PM	8.0

SW W NW  
210 240 270 300  
☉ 253°W (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 9ft



Hopper and push boat staged in Canal CC-CC between stations 1+00 and 1+50





☀ 178°S (T) ● 26°7'58"N, 81°47'10"W ±114ft ▲ 0ft



13 Jul 2022, 09:02:41

Door tag attached to Canal W-W resident's front door



☀ 197°S (T) ● 26°8'15"N, 81°47'16"W ±49ft ▲ 8ft



Removed material at dewatering site at 1300 Curlew Avenue

SW W NW  
210 240 270 300  
☀ 253°W (T) ● 26°8'13"N, 81°47'16"W ±39ft ▲ 8ft



Push boat traveling from Canal CC-CC to Canal X-X

SW

240

W

270

NW

300

330

☉ 283°W (T) ☉ 26°8'4"N, 81°47'15"W ±22ft ▲ 10ft



13 Jul 2022, 13:38:24

Contractor pumping water out from bottom of barge outside the mouth of Canal X-X

N 0 30 NE 60 E 90  
☉ 44°NE (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 12ft



326 excavator transferring removed material from dewatering site to dump truck bed at 1300 Curlew Avenue



**DAILY REPORT OF CONSTRUCTION**  
 21-036 EAST NAPLES BAY  
 DREDGING AND ROCK REMOVAL PROJECT



Date: <b>07/14/2022</b>			
Inspectors: <b>SB</b>	Stantec PIN: <b>2028113191</b>	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: <b>Thursday</b>	Contract Day: <b>270/365</b>	Week: <b>39</b>	Accident Report #: <b>N/A</b>
High Temp (°F): <b>88°F</b>	AM Conditions: <b>Sunny</b>	PM Conditions: <b>Sunny</b>	High Tide: <b>1:27 PM +3.5'</b>
Low Temp (°F): <b>78°F</b>	Wind: <b>5 mph</b>	Wind: <b>11 mph</b>	Low Tide: <b>8:01 AM +1.3'</b>
Canal Worked In: <b>X-X</b>	Stations Worked Between:	<b>0+25 to 0+75</b>	

<b>General</b>
<p><b>#1 – Prime Contractor – Quality Enterprises:</b></p> <ul style="list-style-type: none"> <li>• Contractor has a barge, an excavator, and a hopper stationed outside the mouth of Canal X-X. Contractor also has a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a support boat, a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.</li> <li>• Contactor transported support boat to Jersey barriers on site at 1300 Curlew Avenue.</li> <li>• Dump truck came to site at 1300 Curlew Avenue.</li> <li>• Contractor used 326 excavator to redistribute removed material at dewatering site as well as to transfer removed material from dewatering site to dump truck bed.</li> <li>• Dump truck took removed material off site.</li> <li>• Mechanic came to site at 1300 Curlew Avenue to inspect support boat motor.</li> <li>• Contractor installed turbidity curtain across the mouth of Canal X-X.</li> <li>• Contractor used 323 excavator to remove 2 hoppers of material between stations 0+25 and 0+75.</li> <li>• Contractor used push boat to position barge as necessary for removing material as well as to transport full hoppers of material to Canal CC-CC and empty hoppers of material to Canal X-X</li> <li>• Contractor used 326 excavator to transfer 2 hoppers of material from hopper to dewatering site at 1300 Curlew Avenue.</li> </ul>

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: <b>Quality Enterprises</b>	PM	0	0	Boat Captain	1	9	Mechanic	1	3
		Excavator Operator	1	9	Truck Driver	1	4	Assistant	1	9
		Technician	0	0	Superintendent	1	0.5	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	3
1	CAT 323	Excavator	1	1	2
1	CAT 326	Excavator	1	1	4
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	1	4
1	FL2474PP	Support Boat	1	0	0
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	1	1	9
1	PB727E	Small Dump truck	0	0	0
1	MB27DQ	Dump truck	0	0	0
1	MB8DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	MB26DQ	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0
1	N8105X	Crane Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:30 AM	To: 4:30 PM	8.0

S 180 SW 240 W 270 300  
☉ 234°SW (T) ☉ 26°8'14"N, 81°47'15"W ±13ft ▲ 8ft



326 excavator transferring removed material from dewatering site to dump truck bed at 1300 Curlew Avenue





☀ 199°S (T) ☉ 26°8'13"N, 81°47'16"W ±16ft ▲ 8ft



Support boat sitting on Jersey barriers on site at 1300 Curlew Avenue

SW W NW  
210 240 270 300 330  
☉ 273°W (T) ☉ 26°8'4"N, 81°47'14"W ±16ft ▲ 9ft



323 excavator removing material from station 0+75 and transferring to hopper

SW                      W                      NW                      N  
240                      270                      300                      330                      0

☉ 291°W (T)    ☉ 26°8'4"N, 81°47'15"W ±68ft    ▲ 8ft




323 excavator removing material from station 0+75 and transferring to hopper

E 150 S 180 210 SW 240 W 270  
☀ 207°SW (T) ● 26°8'13"N, 81°47'16"W ±45ft ▲ 8ft



**Mechanic working on support boat motor**



☀ 150°SE (T) ● 26°8'13"N, 81°47'16"W ±13ft ▲ 8ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue



☀ 146°SE (T) ● 26°8'14"N, 81°47'16"W ±29ft ▲ 8ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue



☀ 303°NW (T) ● 26°8'4"N, 81°47'15"W ±29ft ▲ 8ft



14 Jul 2022, 15:43:35

323 excavator removing material from station 0+50 and transferring to hopper

W NW N  
240 270 300 330 0  
☀ 301°NW (T) ☉ 26°8'4"N, 81°47'15"W ±19ft ▲ 9ft



323 excavator lifting spud to allow push boat to mobilize barge at station 0+50





**DAILY REPORT OF CONSTRUCTION**  
 21-036 EAST NAPLES BAY  
 DREDGING AND ROCK REMOVAL PROJECT



Date: <b>07/15/2022</b>			
Inspectors: <b>SB</b>	Stantec PIN: <b>2028113191</b>	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: <b>Friday</b>	Contract Day: <b>271/365</b>	Week: <b>39</b>	Accident Report #: <b>N/A</b>
High Temp (°F): <b>91°F</b>	AM Conditions: <b>Sunny</b>	PM Conditions: <b>Cloudy</b>	High Tide: <b>2:22 PM +3.4'</b>
Low Temp (°F): <b>74°F</b>	Wind: <b>7 mph</b>	Wind: <b>11 mph</b>	Low Tide: <b>8:53 AM +1.2'</b>
Canal Worked In: <b>X-X</b>	Stations Worked Between:	<b>0+00 to 0+75</b>	

**General**

**#1 – Prime Contractor – Quality Enterprises:**

- Contractor has a barge, an excavator, and a hopper stationed outside the mouth of Canal X-X. Contractor also has a hopper, and a push boat staged in Canal CC-CC between stations 1+00 and 2+00. In addition, Contractor has a support boat, a long-reach excavator, a water tank, and two fuel cubes staged on the property located at 1300 Curlew Avenue, Naples, FL, 34102.
- Contractor installed turbidity curtain across the mouth of Canal X-X.
- Contractor used 323 excavator to remove 2 hoppers of material between stations 0+00 and 0+75.
- Contractor used push boat to position barge as necessary for removing material as well as to transport full hoppers of material to Canal CC-CC and empty hoppers of material to Canal X-X.
- Contractor used 326 excavator to transfer 2 hoppers of material from hopper to dewatering site at 1300 Curlew Avenue as well as to redistribute removed material at the dewatering site.
- Trash truck came to site at 1300 Curlew Avenue to remove trash from site.
- Contractor used push boat to transport hopper, 323 excavator, and barge back to Canal CC-CC.
- Contractor pumped water out of hoppers.
- Contractor took boat over to city dock.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: <b>Quality Enterprises</b>	PM	0	0	Boat Captain	1	9	Mechanic	0	0
		Excavator Operator	1	9	Truck Driver	1	1	Assistant	1	9
		Technician	0	0	Superintendent	0	0	VP	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	5
1	CAT 323	Excavator	1	1	4
1	CAT 326	Excavator	1	1	4
1	02016	Front End Loader	0	0	0
1	FL6223TB	Push Boat	1	1	6
1	FL2474PP	Support Boat	1	0	0
1	N3758Z	Fuel Truck	0	0	0
1	P9457E	Water Truck	0	0	0
1	725RZM	Water Tank	1	0	0
1	Z68EAZ	Small Dump truck	0	0	0
1	PB727E	Small Dump truck	0	0	0
1	Z67EAZ	Trash Truck	1	1	1
1	MB27DQ	Dump truck	0	0	0
1	MB8DQ	Dump truck	0	0	0
1	MB30DQ	Utility Truck	0	0	0
1	MB26DQ	Utility Truck	0	0	0
1	N9524Z	Transport Truck	0	0	0
1	044RTN	Welding Truck	0	0	0
1	N8105X	Crane Truck	0	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Sam Boyd, EIT	From: 8:30 AM	To: 4:30 PM	8.0

SW 240 W 270 NW 330 N 0

☉ 291°W (T) ☉ 26°8'4"N, 81°47'15"W ±42ft ▲ 9ft



323 excavator lifting spud to allow push boat to mobilize barge at station 0+50



☀ 304°NW (T) ● 26°8'4"N, 81°47'15"W ±16ft ▲ 9ft



15 Jul 2022, 07:59:18

323 excavator removing material from station 0+25

SW W NW  
210 240 270 300  
☉ 254°W (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 10ft



Push boat transporting full hopper of removed material from Canal X-X to Canal CC-CC



☉ 177°S (T) ☉ 26°8'14"N, 81°47'16"W ±13ft ▲ 7ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue

SE S SW  
120 150 180 210 240  
☀ 188°S (T) ☉ 26°8'14"N, 81°47'15"W ±32ft ▲ 8ft



326 excavator transferring removed material from hopper to dewatering site at 1300 Curlew Avenue



15 Jul 2022, 11:03:17

Trash truck on site at 1300 Curlew Avenue



SE S SW  
120 150 180 210 240

☀ 188°S (T) ☉ 26°8'14"N, 81°47'16"W ±16ft ▲ 9ft



326 excavator moving support boat to southwest corner of 1300 Curlew Avenue

SW W NW  
210 240 270 300 330  
☀ 277°W (T) ☉ 26°8'5"N, 81°47'15"W ±95ft ▲ 9ft



15 Jul 2022, 13:37:34

323 excavator lifting spud to allow push boat to transport barge and 323 excavator from Canal X-X to Canal CC-CC



☉ 147°SE (T) ☉ 26°8'13"N, 81°47'16"W ±13ft ▲ 10ft



**Barge, 323 excavator, and 2 hoppers staged in Canal CC-CC between stations 1+00 and 1+50**
